

# Campus Master Plan Update January 8, 2014



Harper College®



# Building D: Phase 1

- On Schedule: Fall 2014 Semester  
(pending Regional Generator Completion)
- Under Budget

# Building D: Phase 1



# Building D: Phase 1





# Building H

- On Schedule: Spring 2015 Semester
- Under Budget
- Change Order Timing: 4 Months per CDB
- CDB/CPO Relationship



# Building H





# East Campus Parking Structure

- On Schedule: Reconfigured Lot 6 and 2 Floors Open August 2014, Balance by October 2014
- On Budget
- Kris Howard Drive Reconfiguration Completion Targeted for August 2014, Pending Change Order Approval (in Progress)



# East Campus Parking Structure







# East Campus Landscaping Project

- Phased Implementation
- Sustainable Design Consistent with New North Campus Site Improvements
- Collaborating with Green Committee and Biology Department



# Building E – E106

- On Schedule: Construction Complete, IT Installation in Progress
- Budget: Funded from Contingency, Insurance Subrogation in Process (greater than \$500K)

# Building E – E106





# Building E – E106






# Advanced Manufacturing Lab

- On Schedule: Design in Progress,  
Targeting Completion Fall 2015 Semester

# Advanced Manufacturing Lab

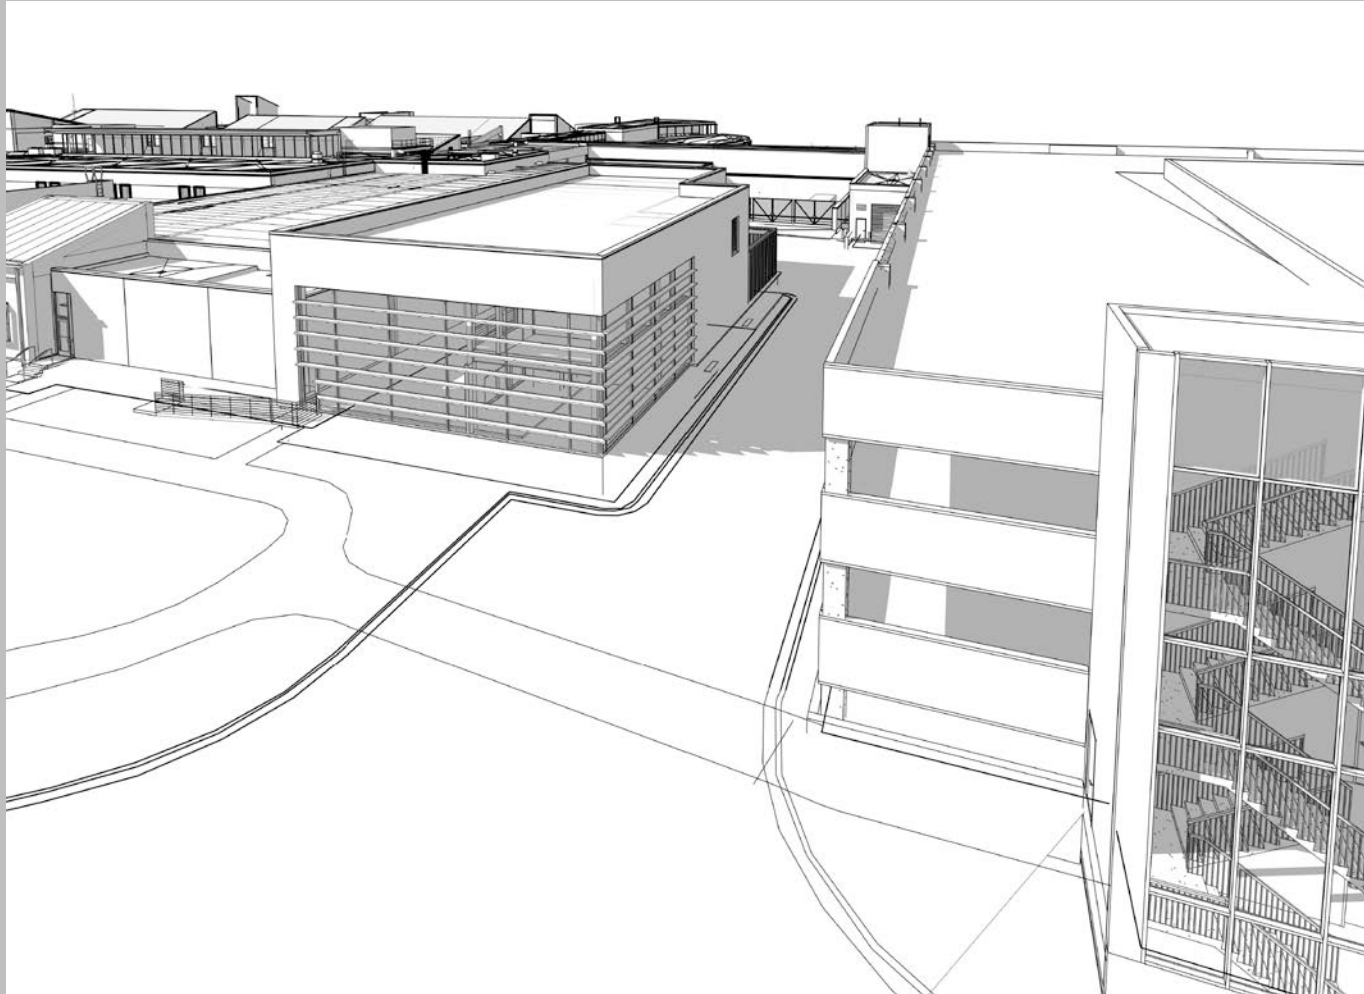






# One Stop/Student Center

- Schematic Design Complete. Design Development to Start Late-January 2014



# West Campus Infrastructure Project

- On Schedule: Design in Progress, Targeting Completion Fall 2016 Semester
