



Harper College

Business and Social Sciences Center

Palatine, Illinois

Board Meeting | January 17, 2024

RAMSA **fgma**
ROBERT A.M. STERN ARCHITECTS

200 ft

AGENDA

1. Design Schedule
2. User Group Meeting Update
3. Review of Schematic Design Drawings

Site Plan

Floor Plans

Elevations

Renderings

4. Pricing Update

PROJECT MILESTONES

TASK	START	END
PROGRAMMING/CONCEPT	November 2022	June 2023
SCHEMATIC DESIGN	June 2023	January 2024

PROJECT MILESTONES

TASK	START	END
PROGRAMMING/CONCEPT	November 2022	June 2023
SCHEMATIC DESIGN	June 2023	January 2024
DESIGN DEVELOPMENT	January 2024	June 2024
CONSTRUCTION DOCUMENTS	June 2024	February 2025

PROJECT MILESTONES

TASK	START	END
PROGRAMMING/CONCEPT	November 2022	June 2023
SCHEMATIC DESIGN	June 2023	January 2024
DESIGN DEVELOPMENT	January 2024	June 2024
CONSTRUCTION DOCUMENTS	June 2024	February 2025
BIDDING & PROCUREMENT	March 2025	May 2025
PHASE 1 - NEW CONSTRUCTION	June 2025	February 2027

PROJECT MILESTONES


TASK	START	END
PROGRAMMING/CONCEPT	November 2022	June 2023
SCHEMATIC DESIGN	June 2023	January 2024
DESIGN DEVELOPMENT	January 2024	June 2024
CONSTRUCTION DOCUMENTS	June 2024	February 2025
BIDDING & PROCUREMENT	March 2025	May 2025
PHASE 1 - NEW CONSTRUCTION	June 2025	February 2027
PHASE 1 - MOVE IN / OCCUPANCY	February 2027	September 2027
PHASE 2 - DEMO EXISTING BUILDINGS	September 2027	December 2027
PHASE 3 - SITE RESTORATION	January 2028	June 2028

PROJECT MILESTONES

TASK	START	END
PROGRAMMING/CONCEPT	November 2022	June 2023
SCHEMATIC DESIGN	June 2023	January 2024
DESIGN DEVELOPMENT	January 2024	June 2024
CONSTRUCTION DOCUMENTS	June 2024	February 2025
BIDDING & PROCUREMENT	March 2025	May 2025
PHASE 1 - NEW CONSTRUCTION	June 2025	February 2027
PHASE 1 - MOVE IN / OCCUPANCY	February 2027	September 2027
PHASE 2 - DEMO EXISTING BUILDINGS	September 2027	December 2027
PHASE 3 - SITE RESTORATION	January 2028	June 2028
CLOSEOUT / FINAL COMPLETION	July 2028	September 2028

PROJECT TIMELINE



- EXECUTIVE CABINET MEETING
- COMMITTEE OF THE WHOLE
- BOARD MEETING
- VIRTUAL USER GROUP MEETINGS
- TEAM SITE VISIT
- CLIENT/SC MEETING

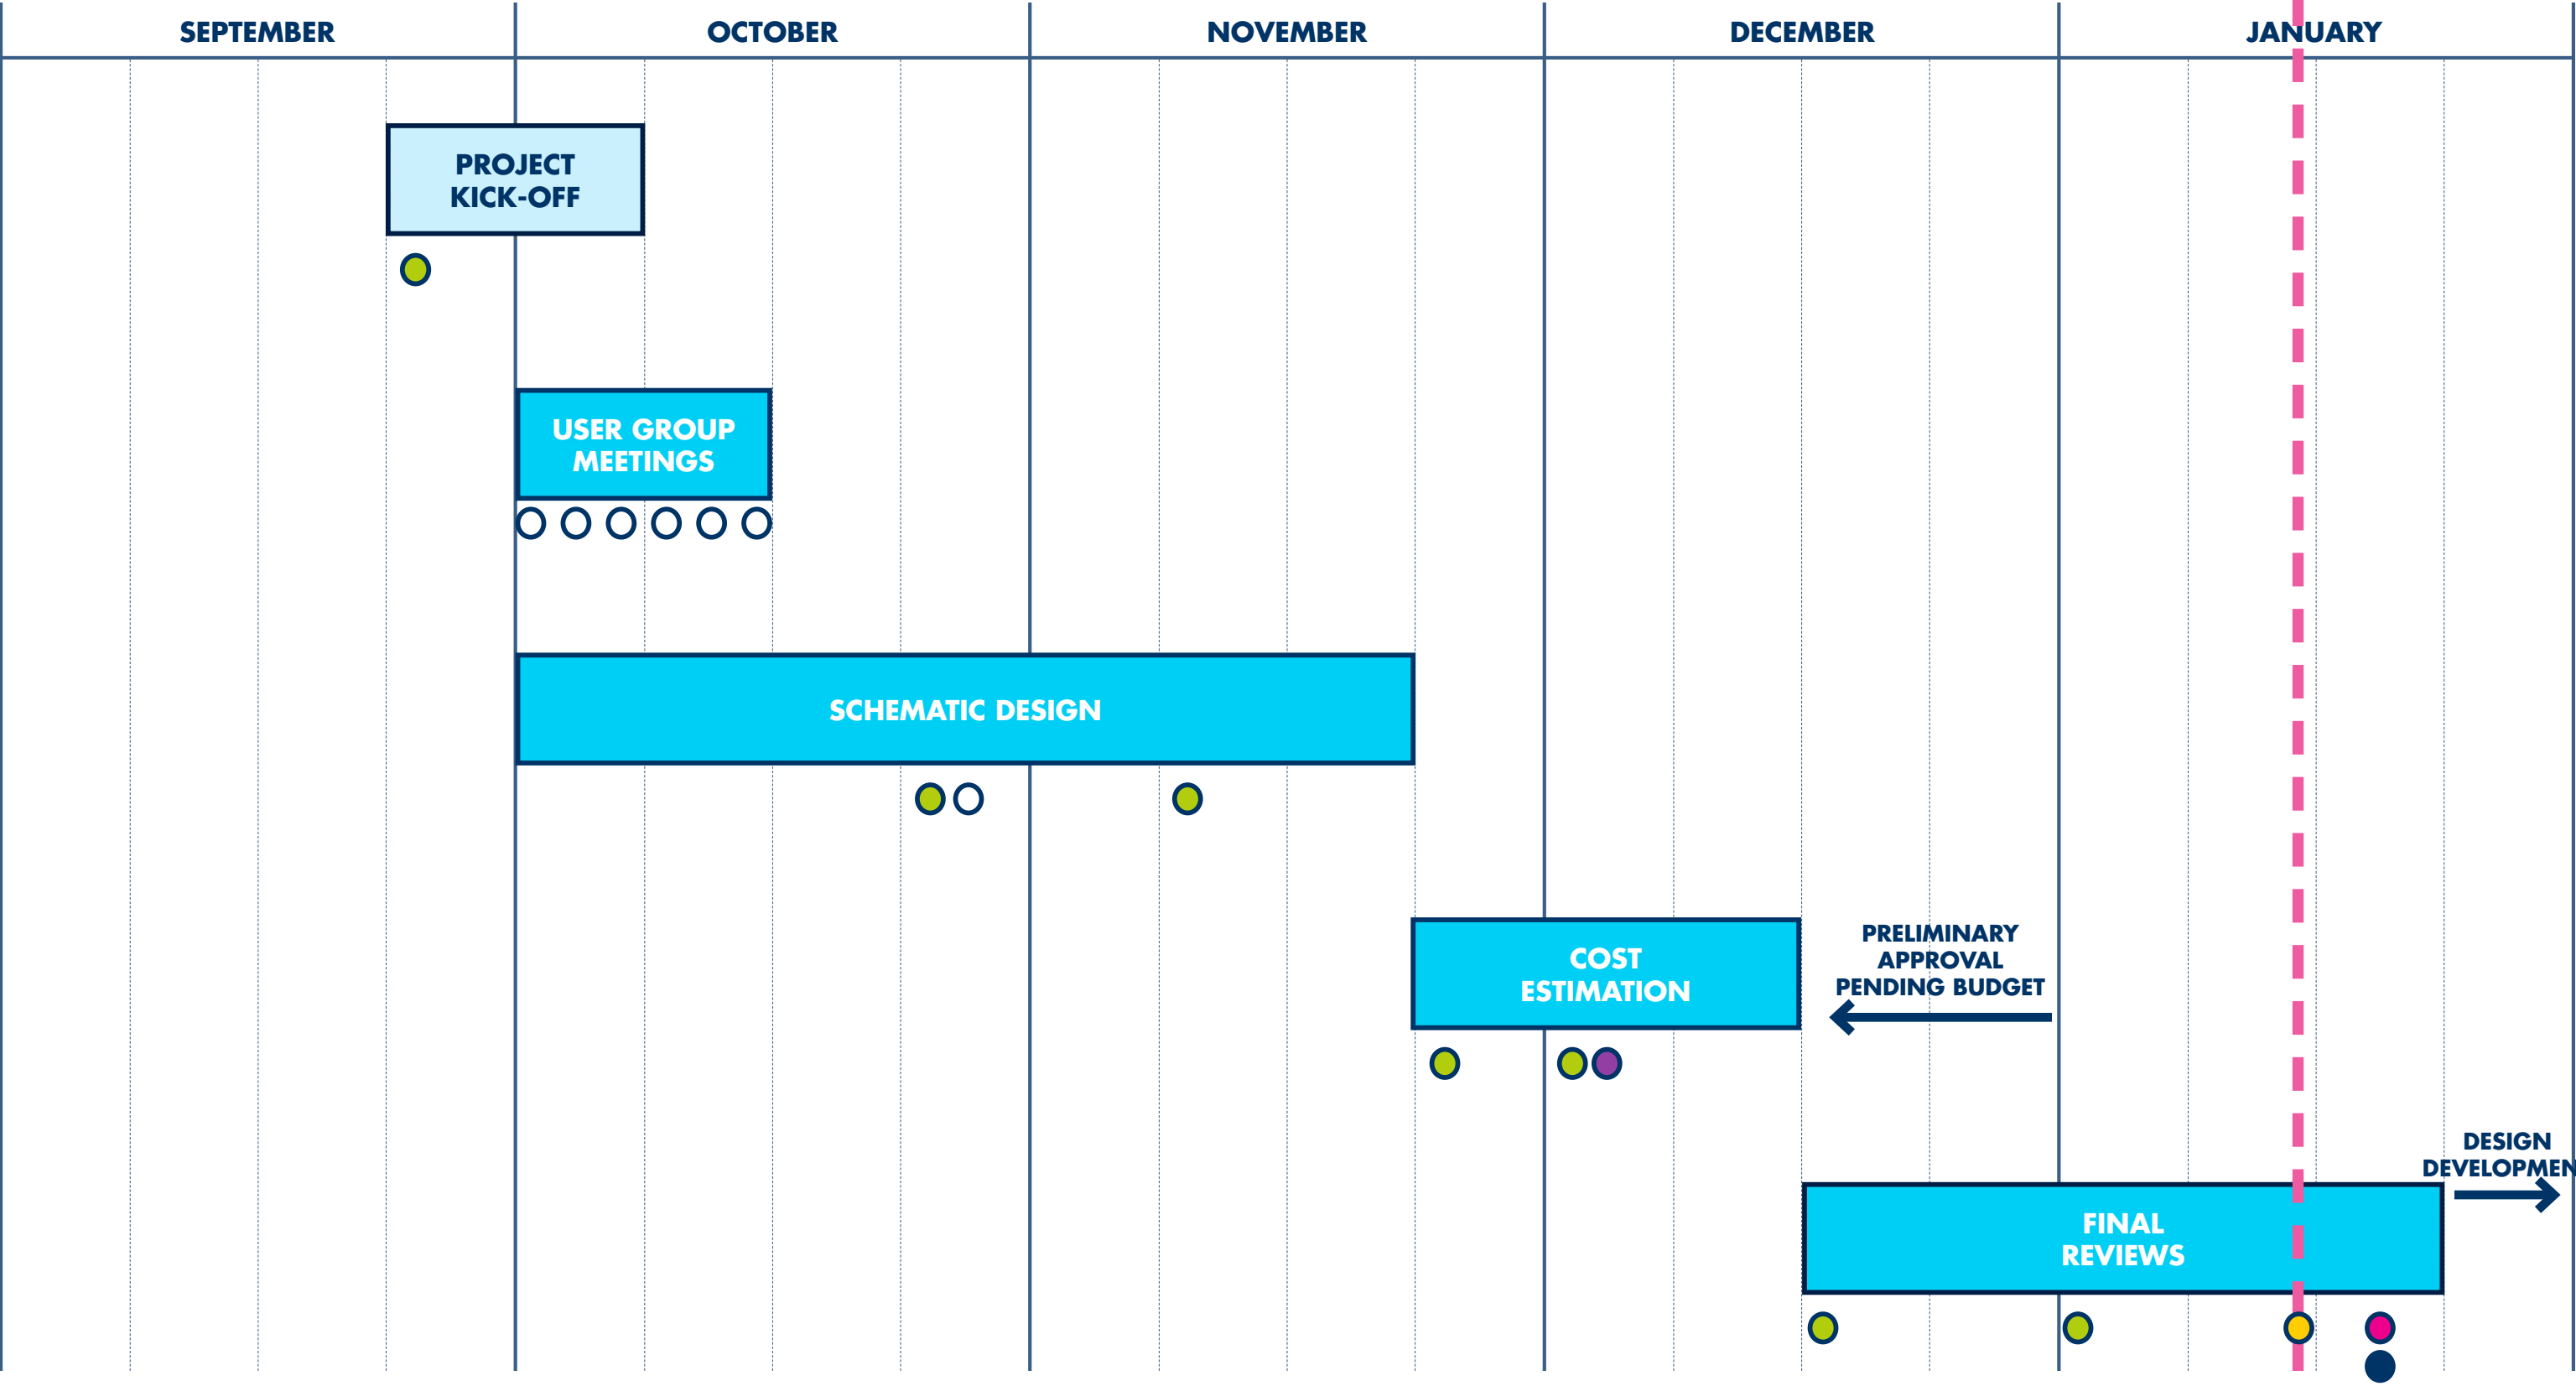










USER GROUP MEETINGS

	Tuesday, October 3	Monday, October 9	Tuesday, October 10	Wednesday, October 11	Thursday, October 12	Wednesday, October 18
8 - 8:50am			Education, History, Political Science			
9 - 9:50am		Geography, GIS, Drone Lab	Early Childhood Education & Lab School		Computer Information Systems	IT
11 - 11:50am	Theater	Police, IT			Artificial Intelligence Aviation & Cyber Security	
1 - 1:50pm			Business, Accounting, Economics		Facilities	
2 - 2:50pm		Paralegal & Studio V		IDEA Center		
3 - 3:50pm				Fast Track		
3:30 - 4:20pm			Social Science			


USER GROUP MEETINGS - EXAMPLE

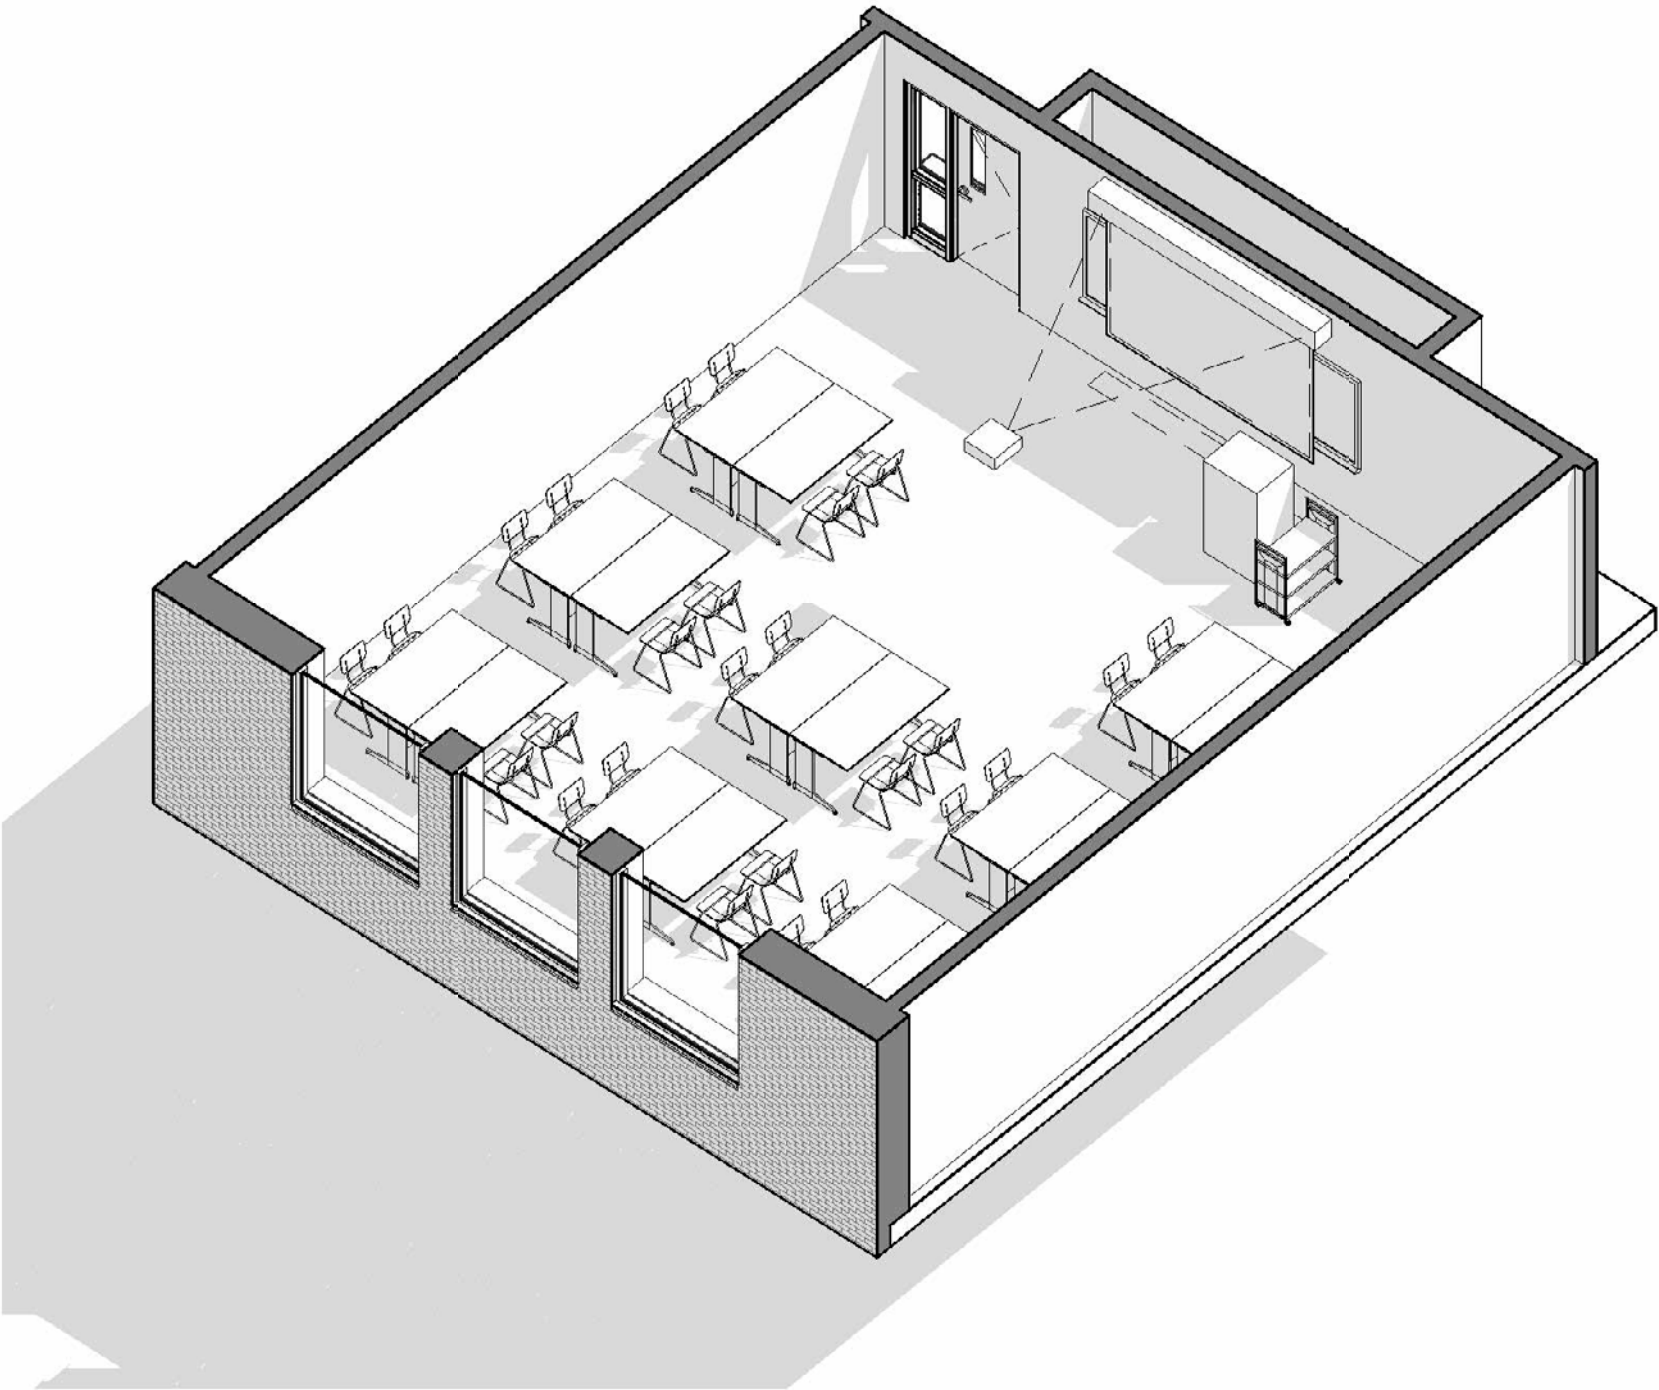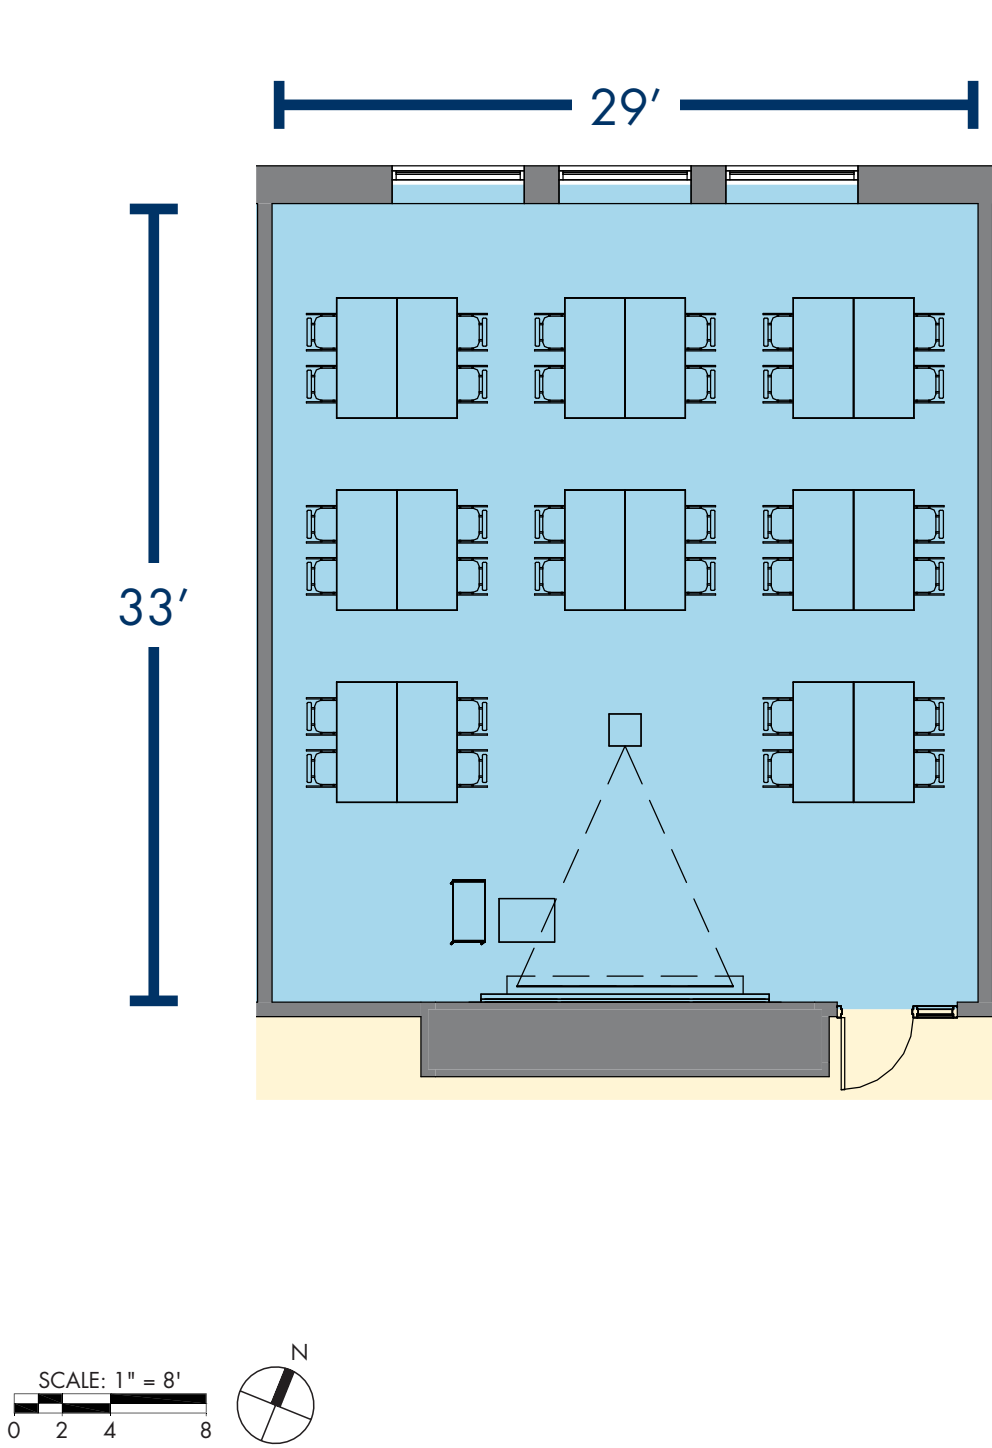


USER GROUP MEETINGS - EXAMPLE

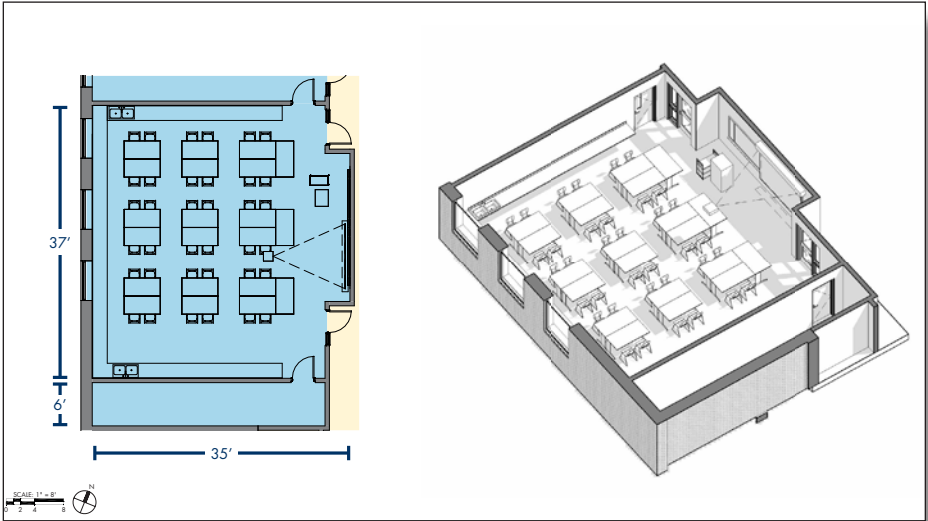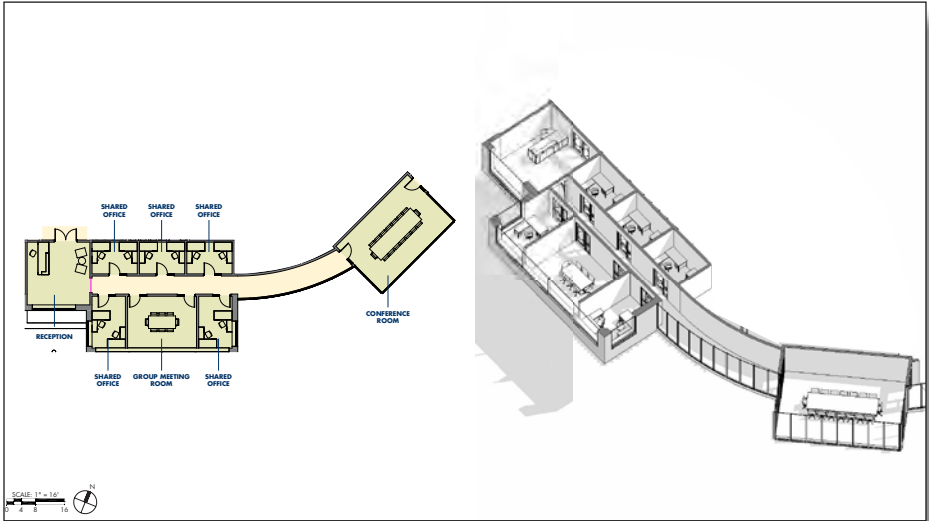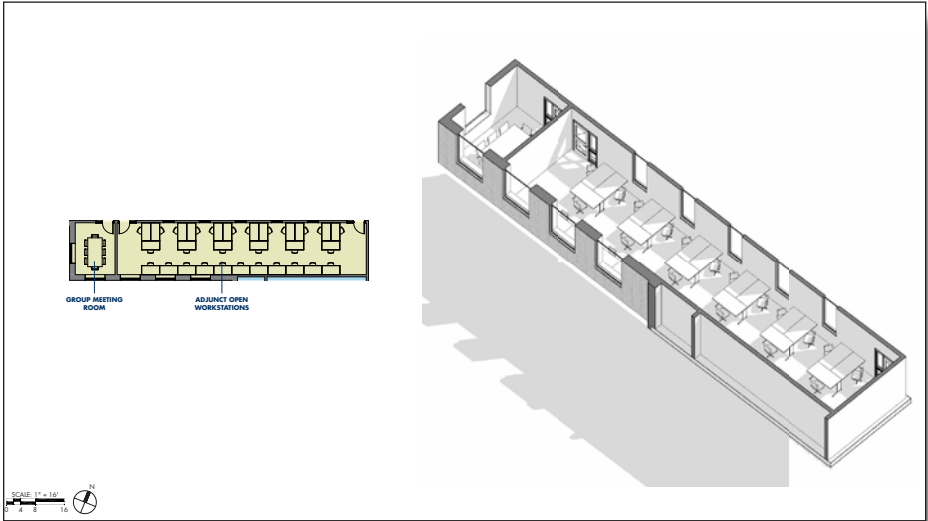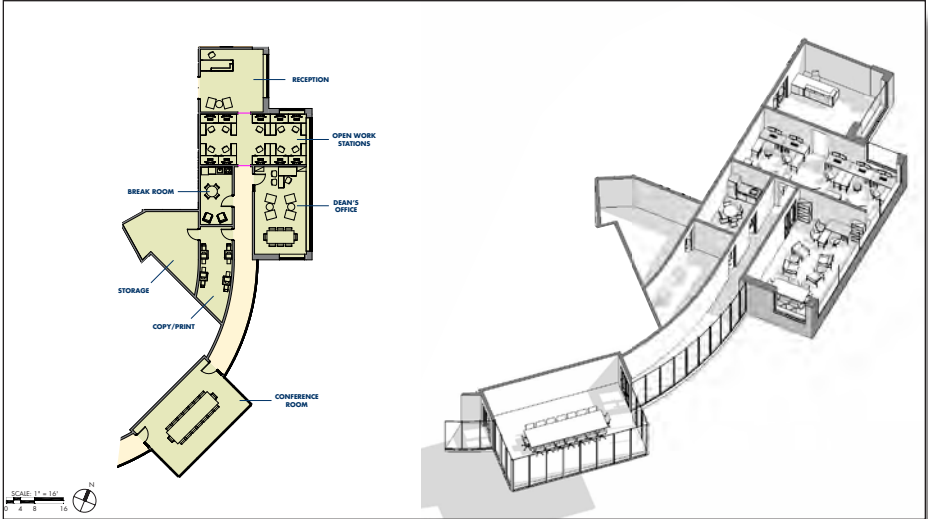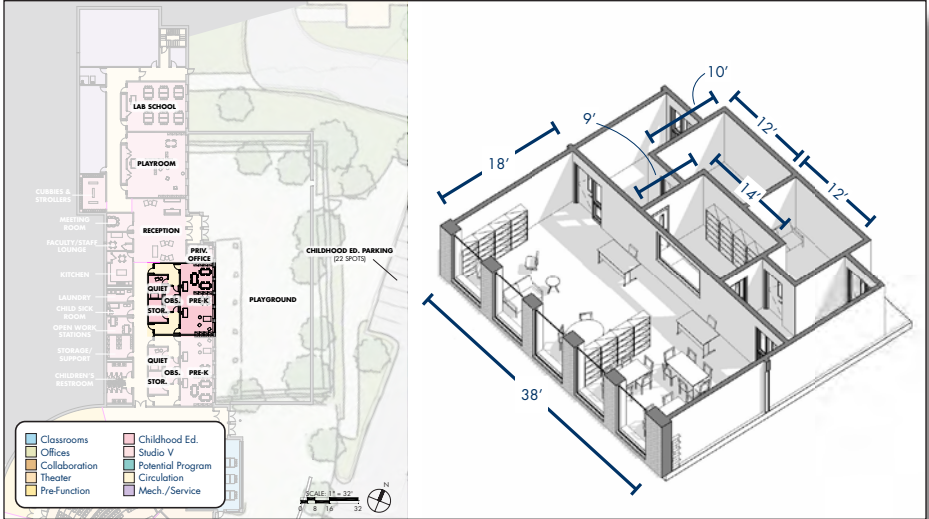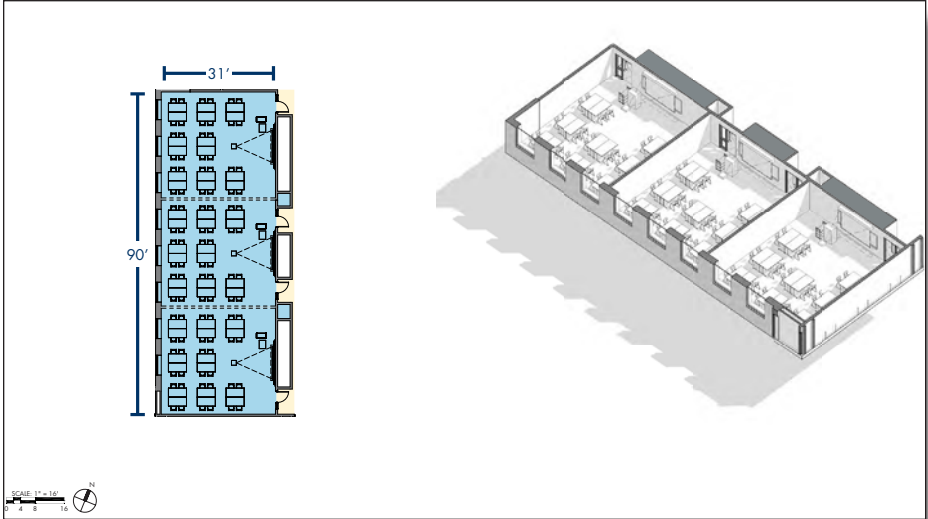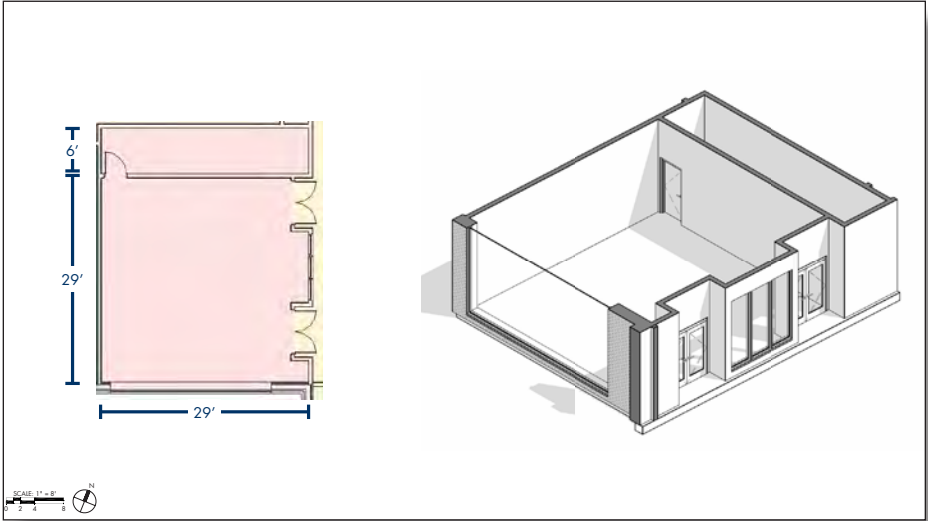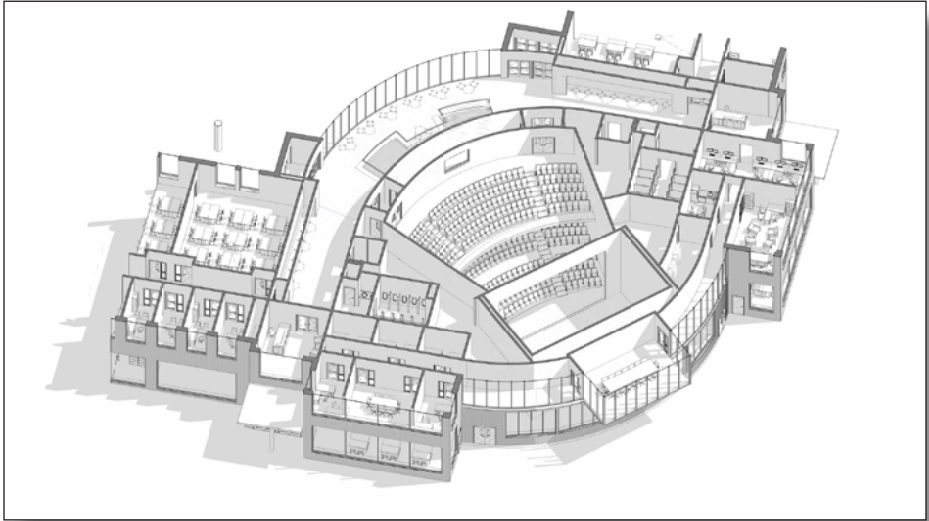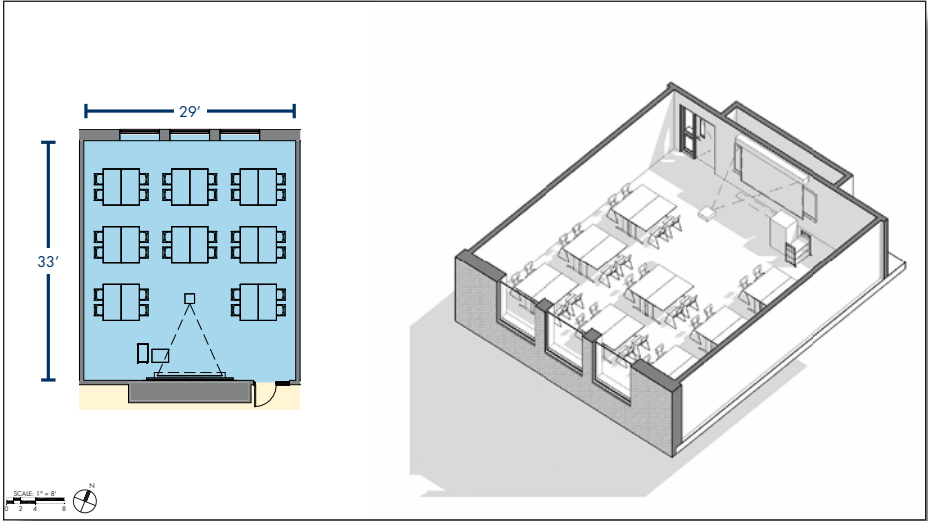


EXISTING SITE PLAN

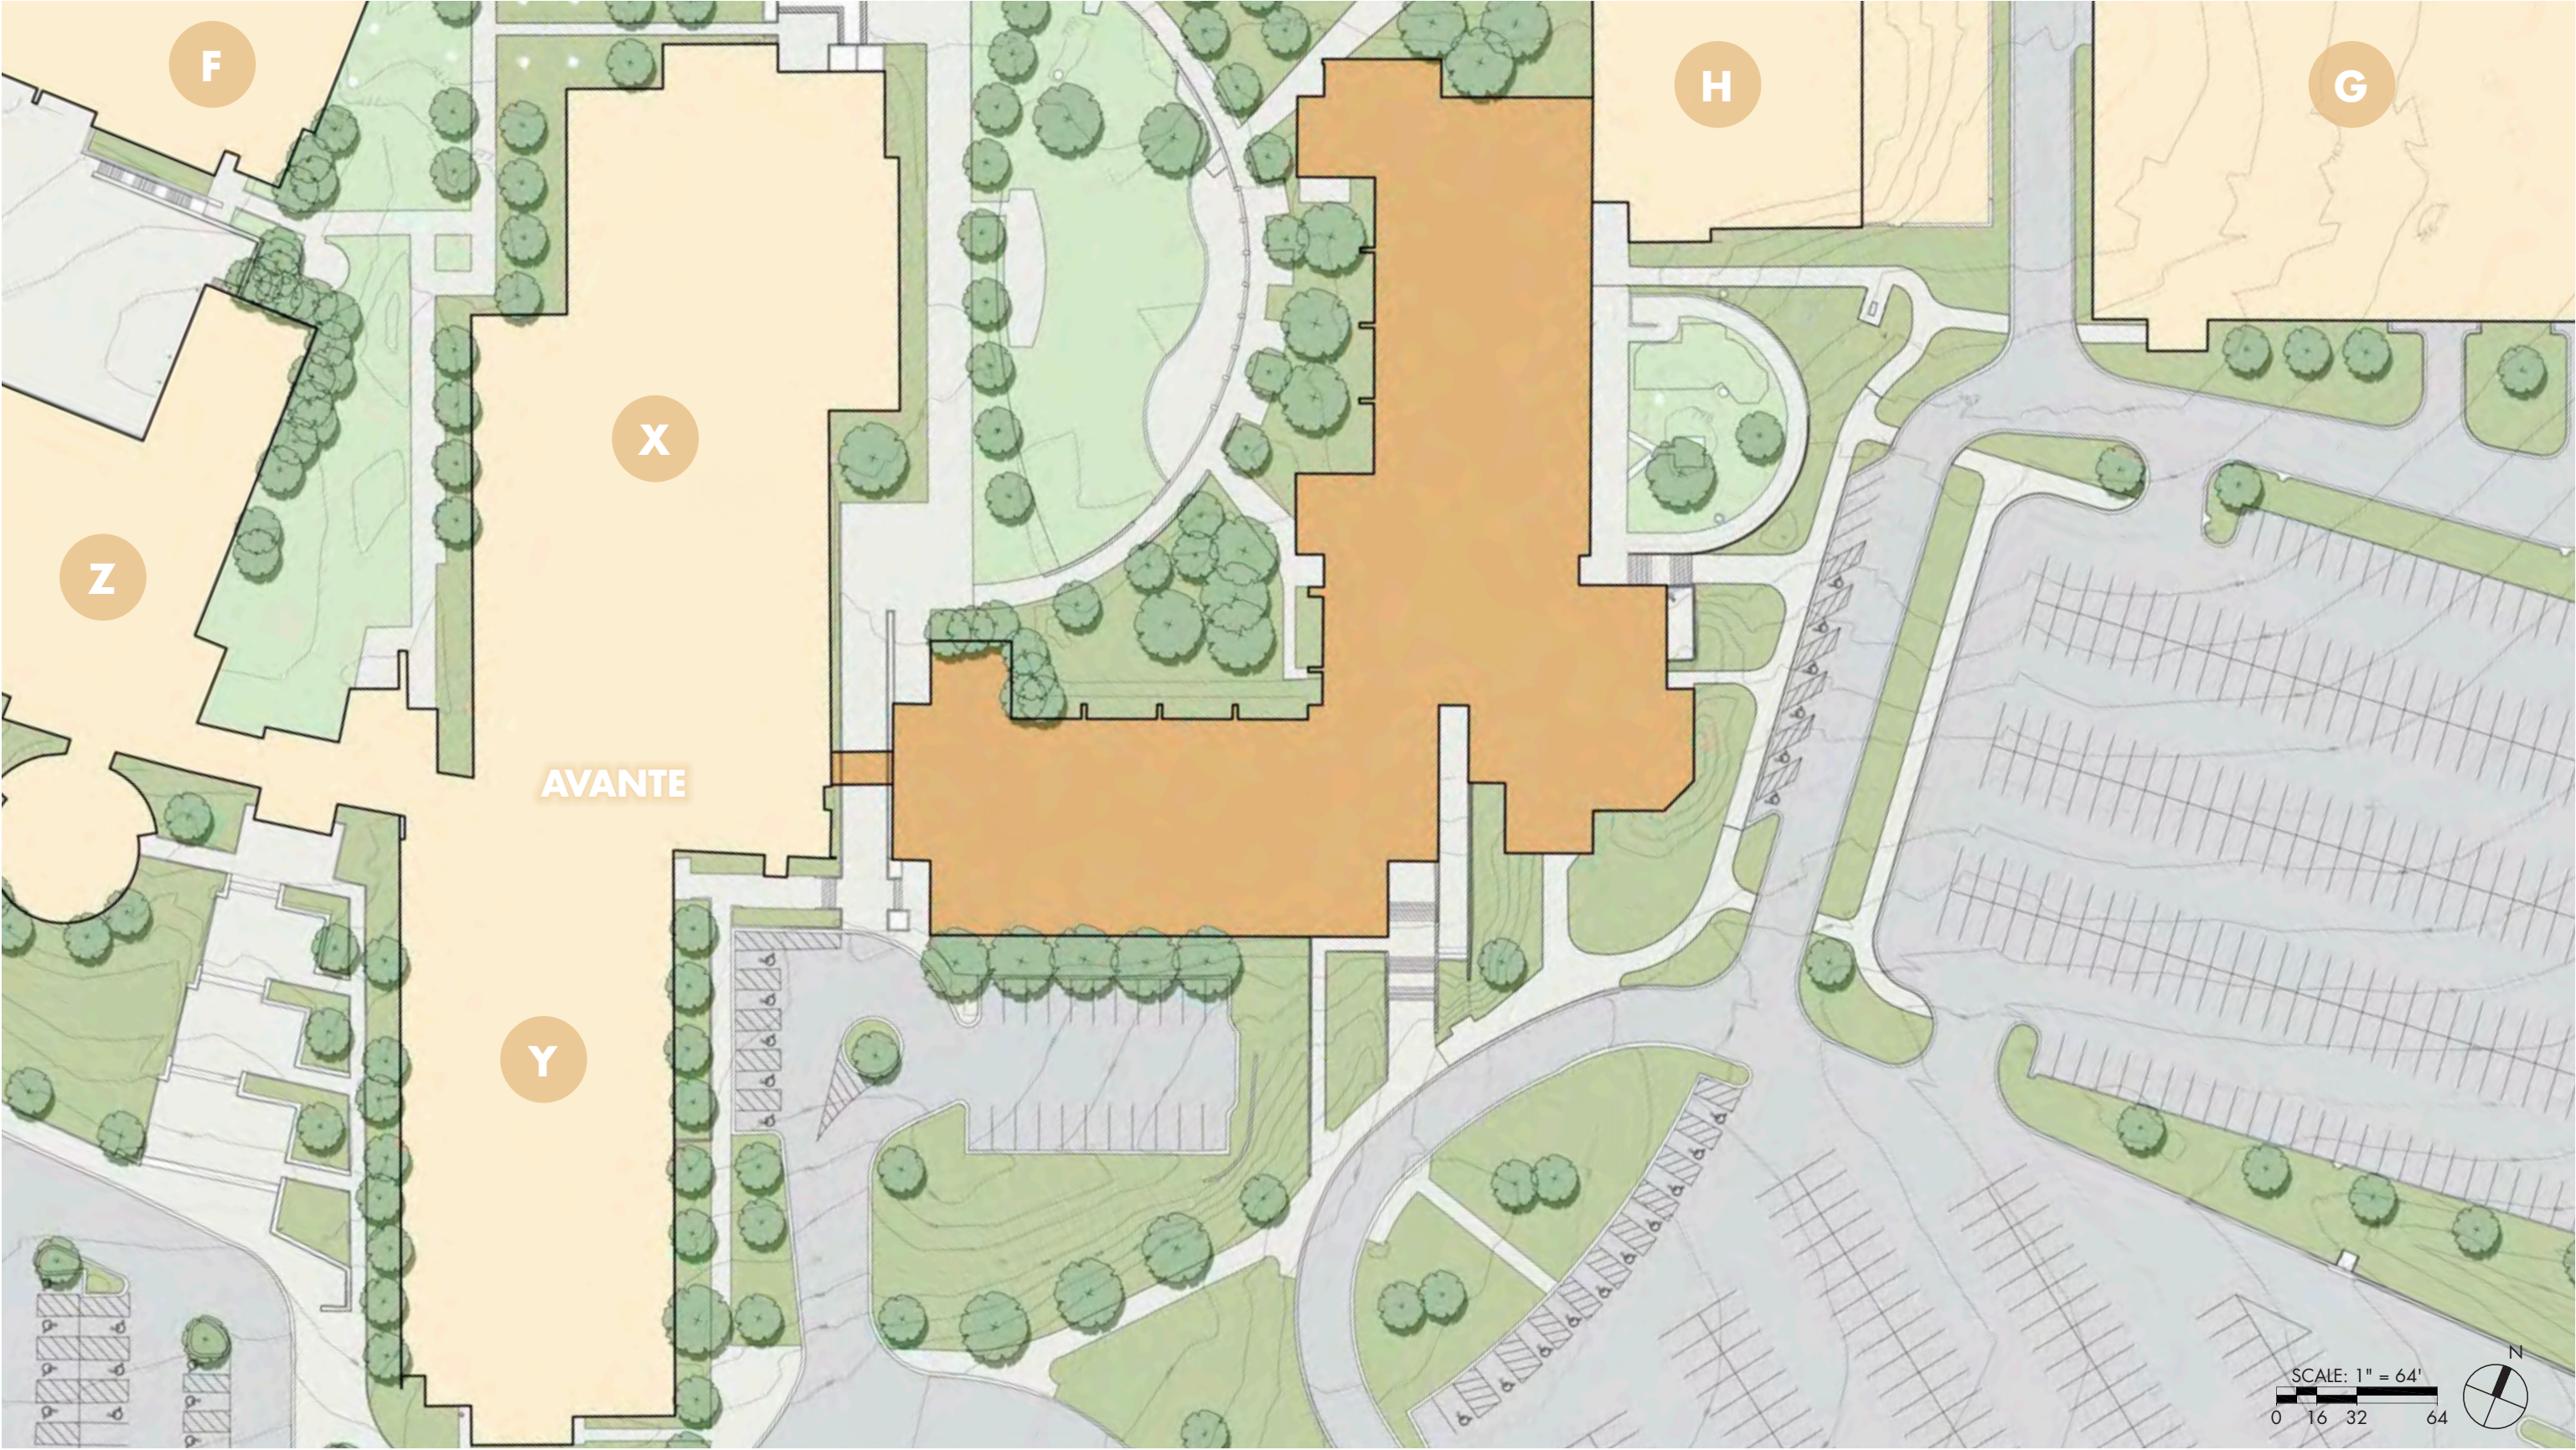


PROPOSED SITE PLAN

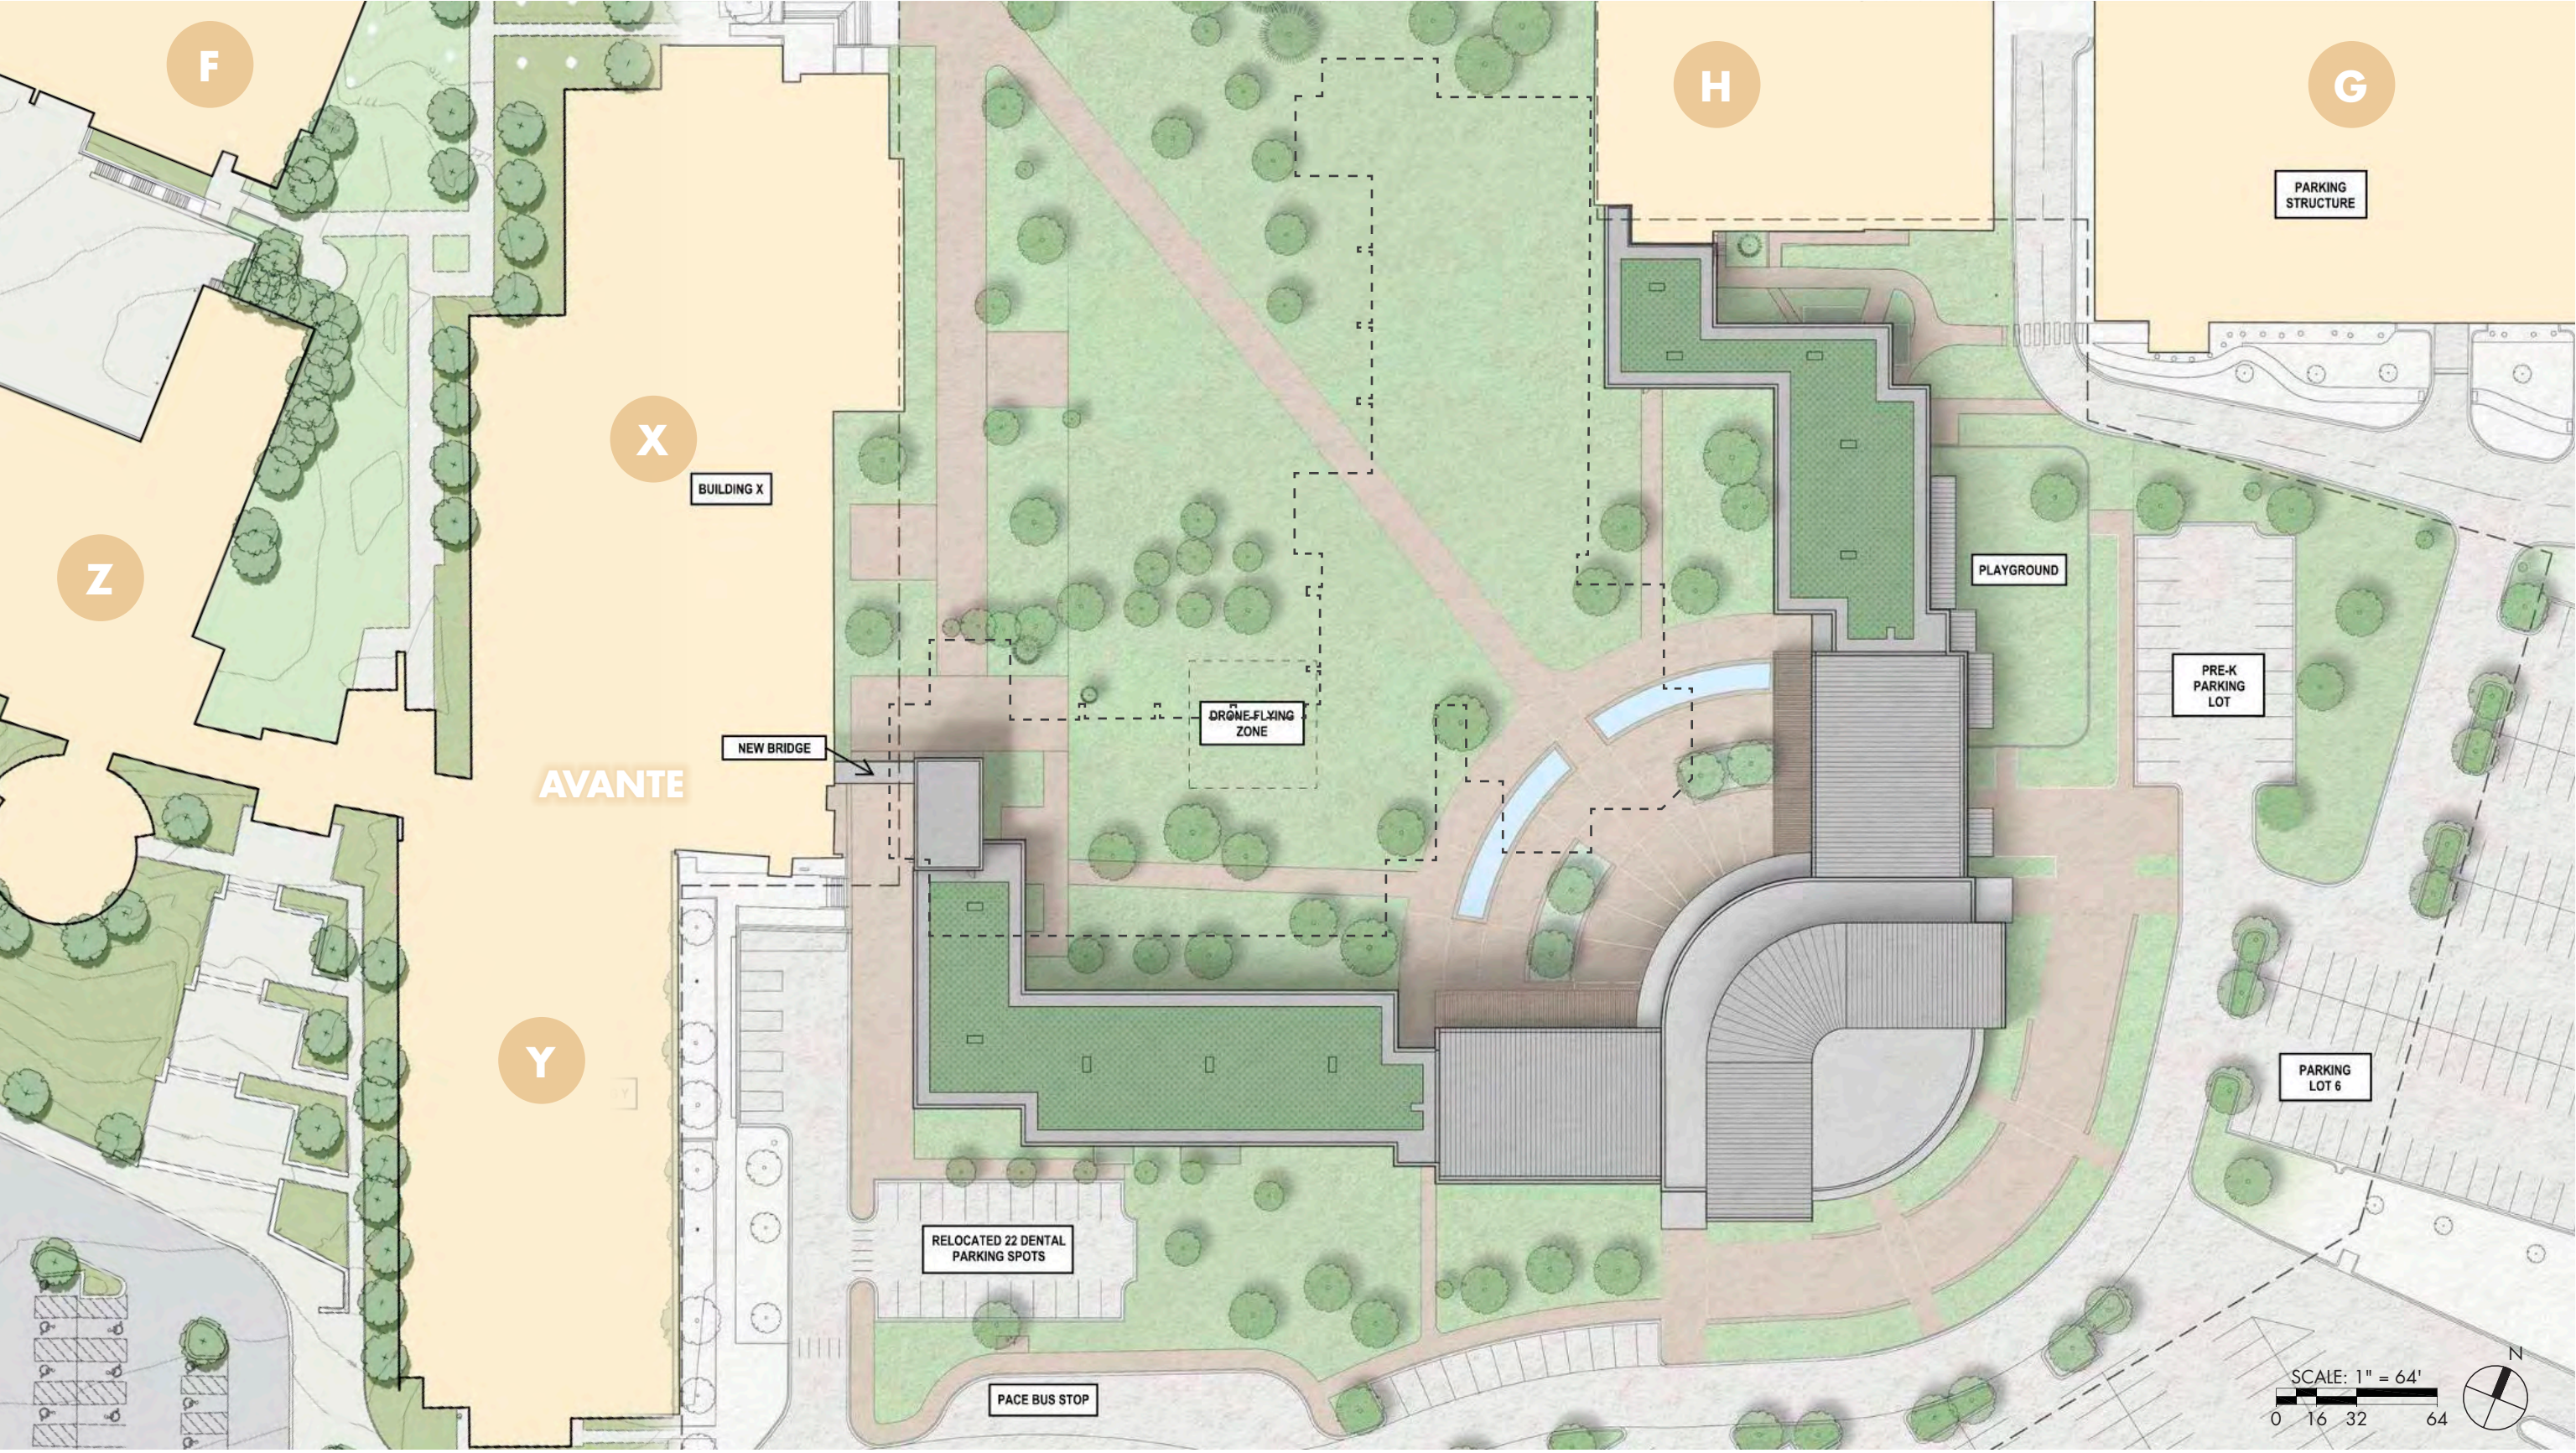

PARKING LEVEL

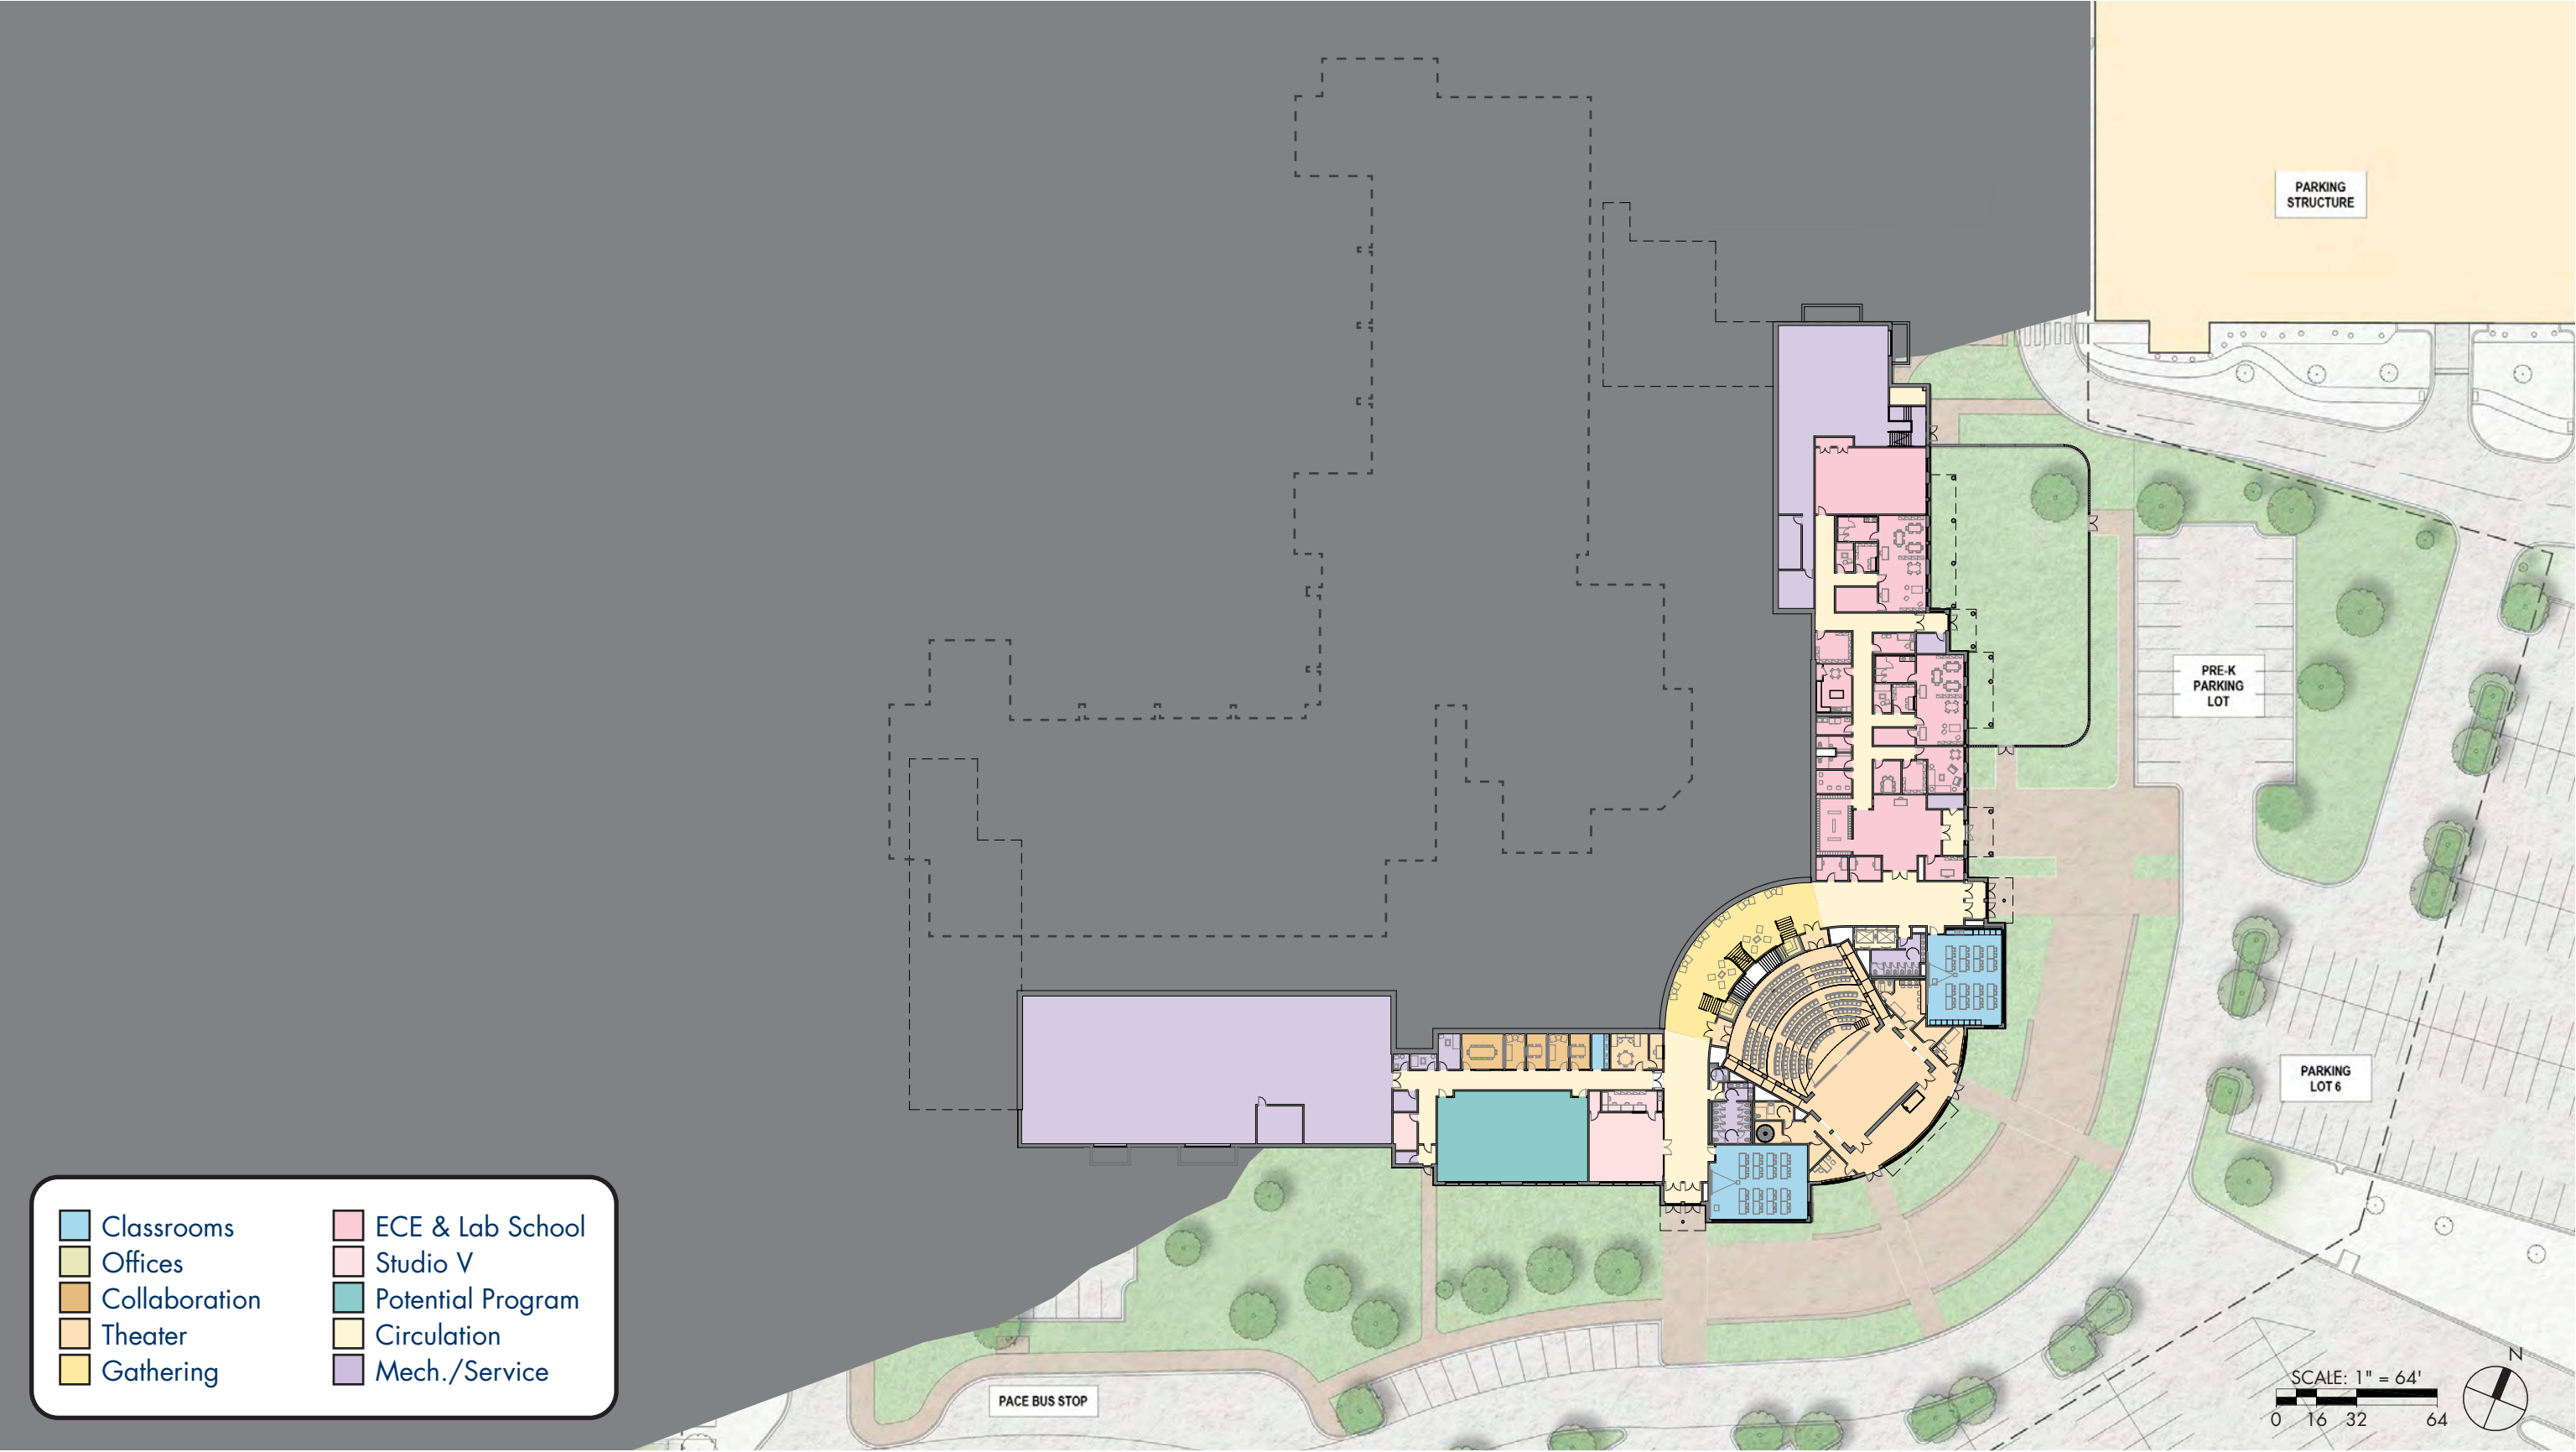


COURTYARD LEVEL

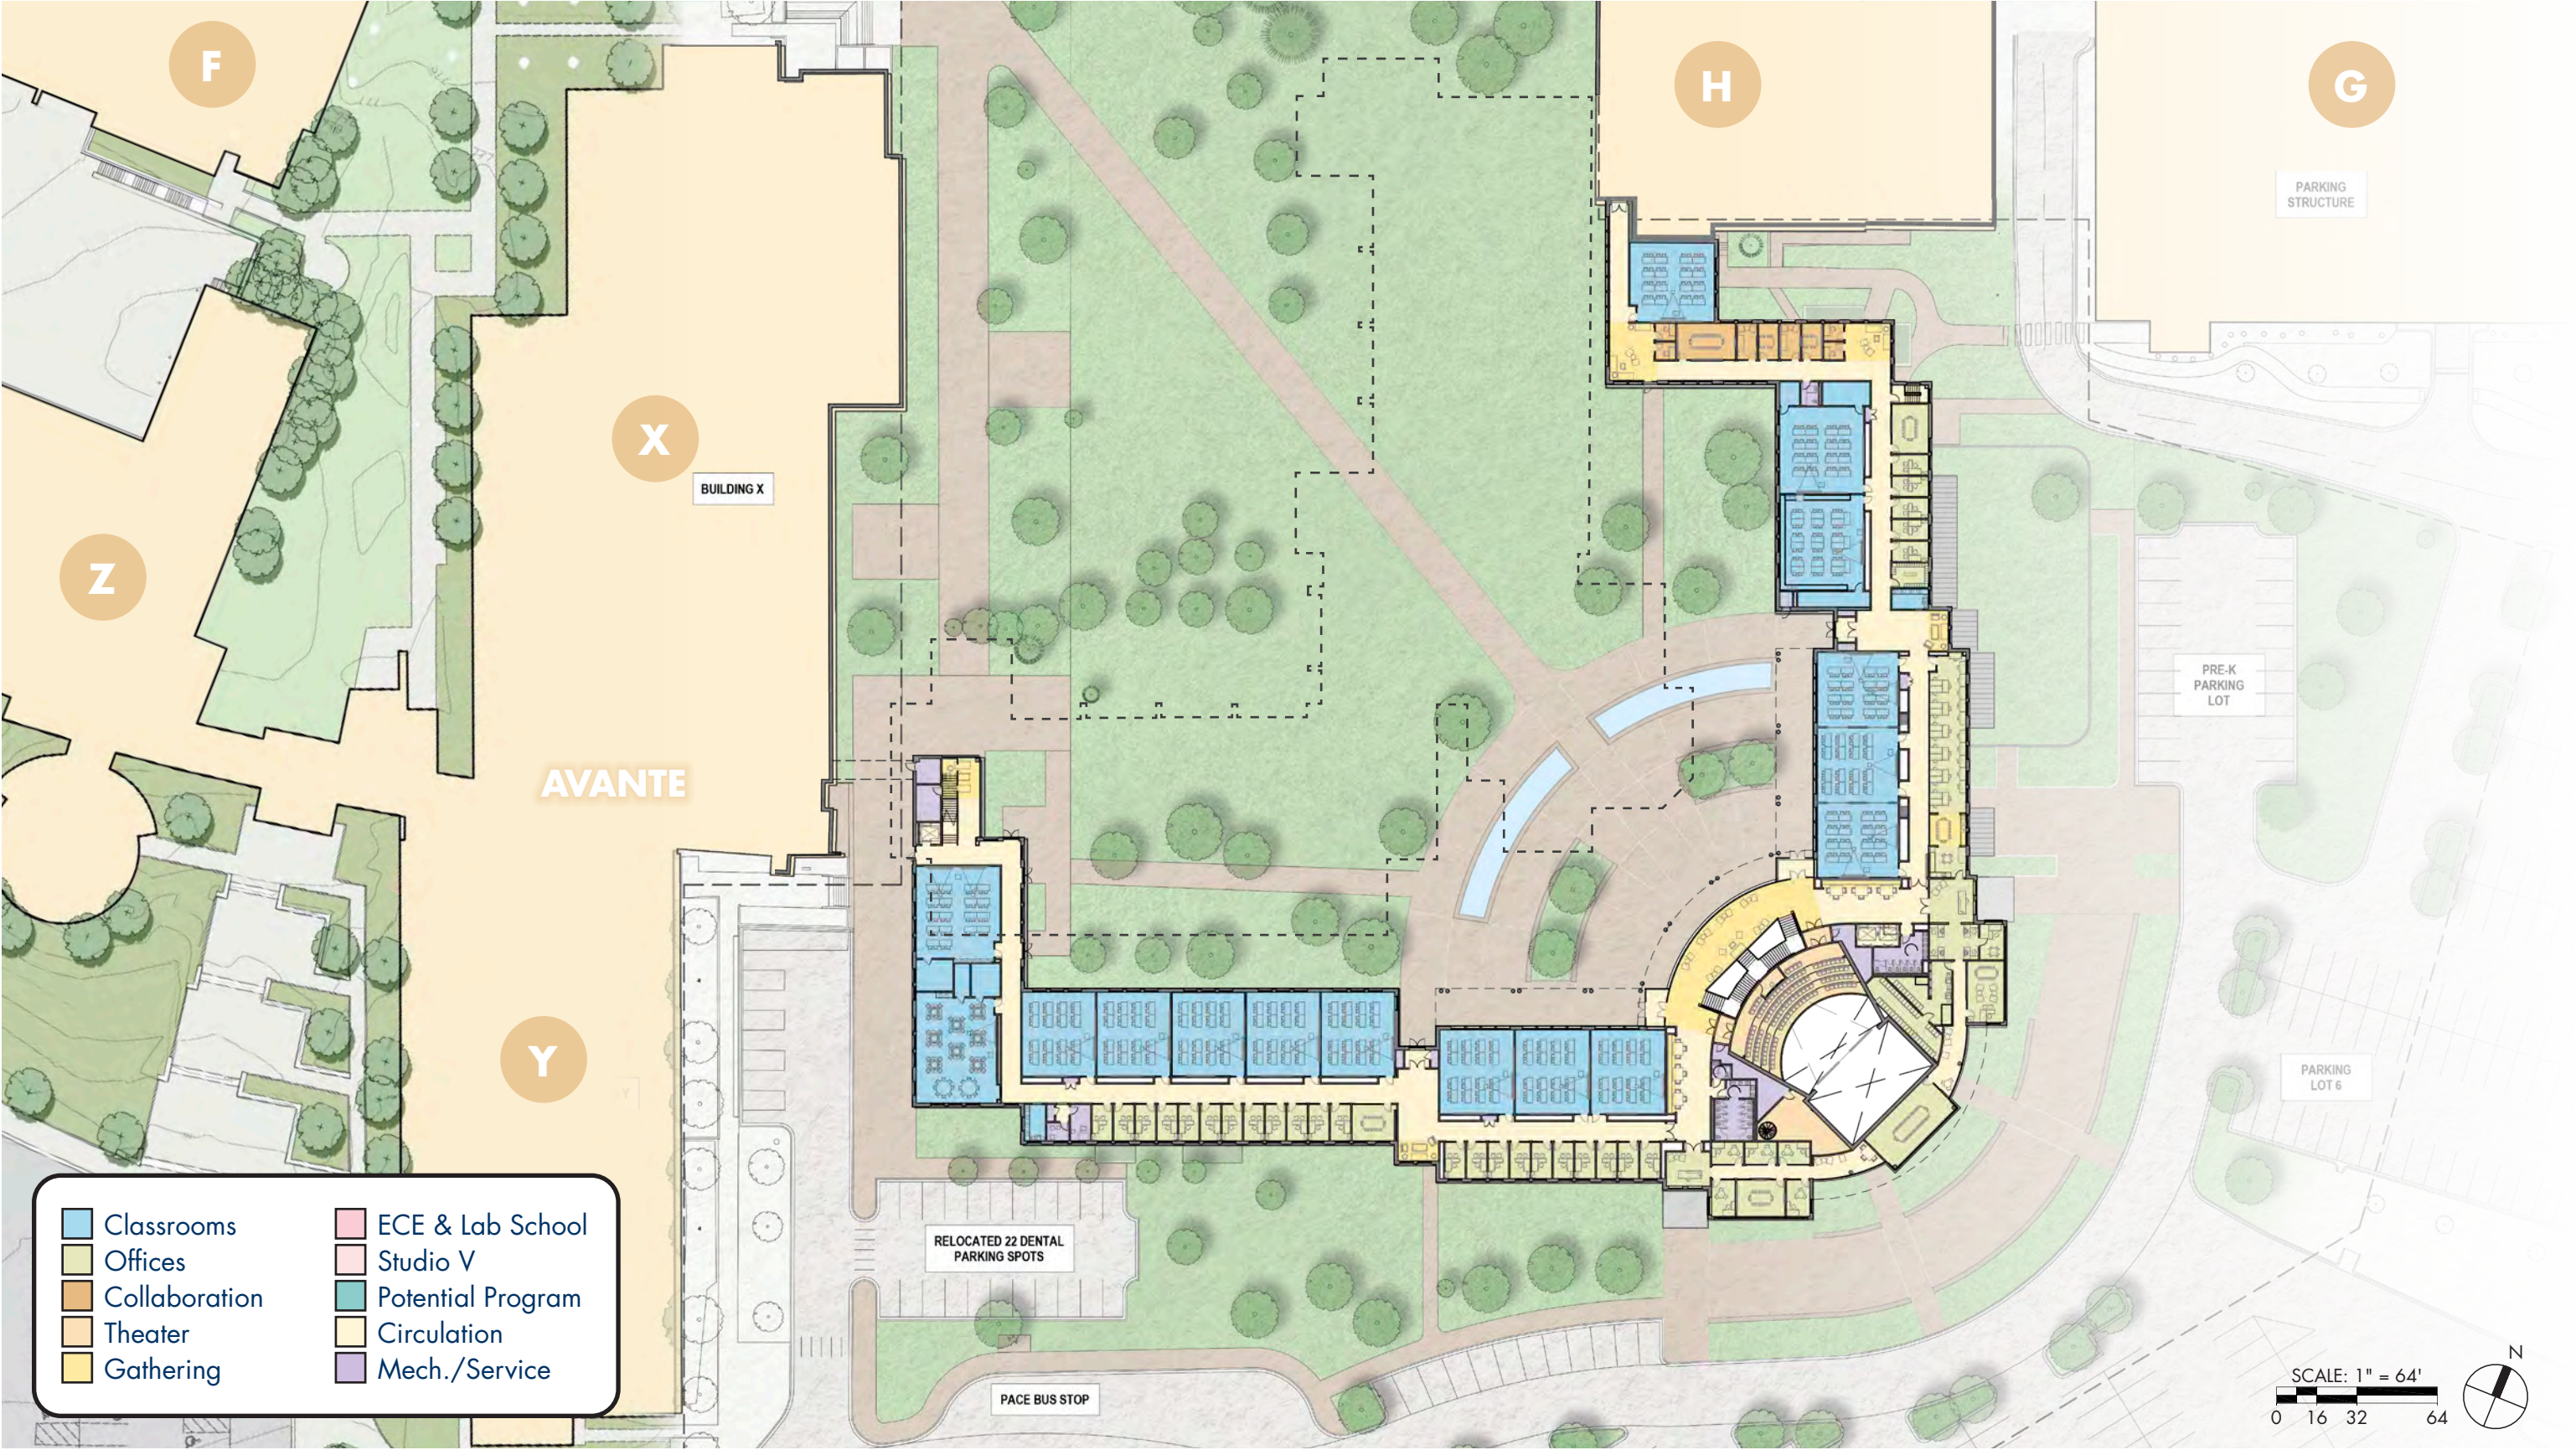


EARLY CHILDHOOD EDUCATION & LAB SCHOOL




THEATER & STUDIO V

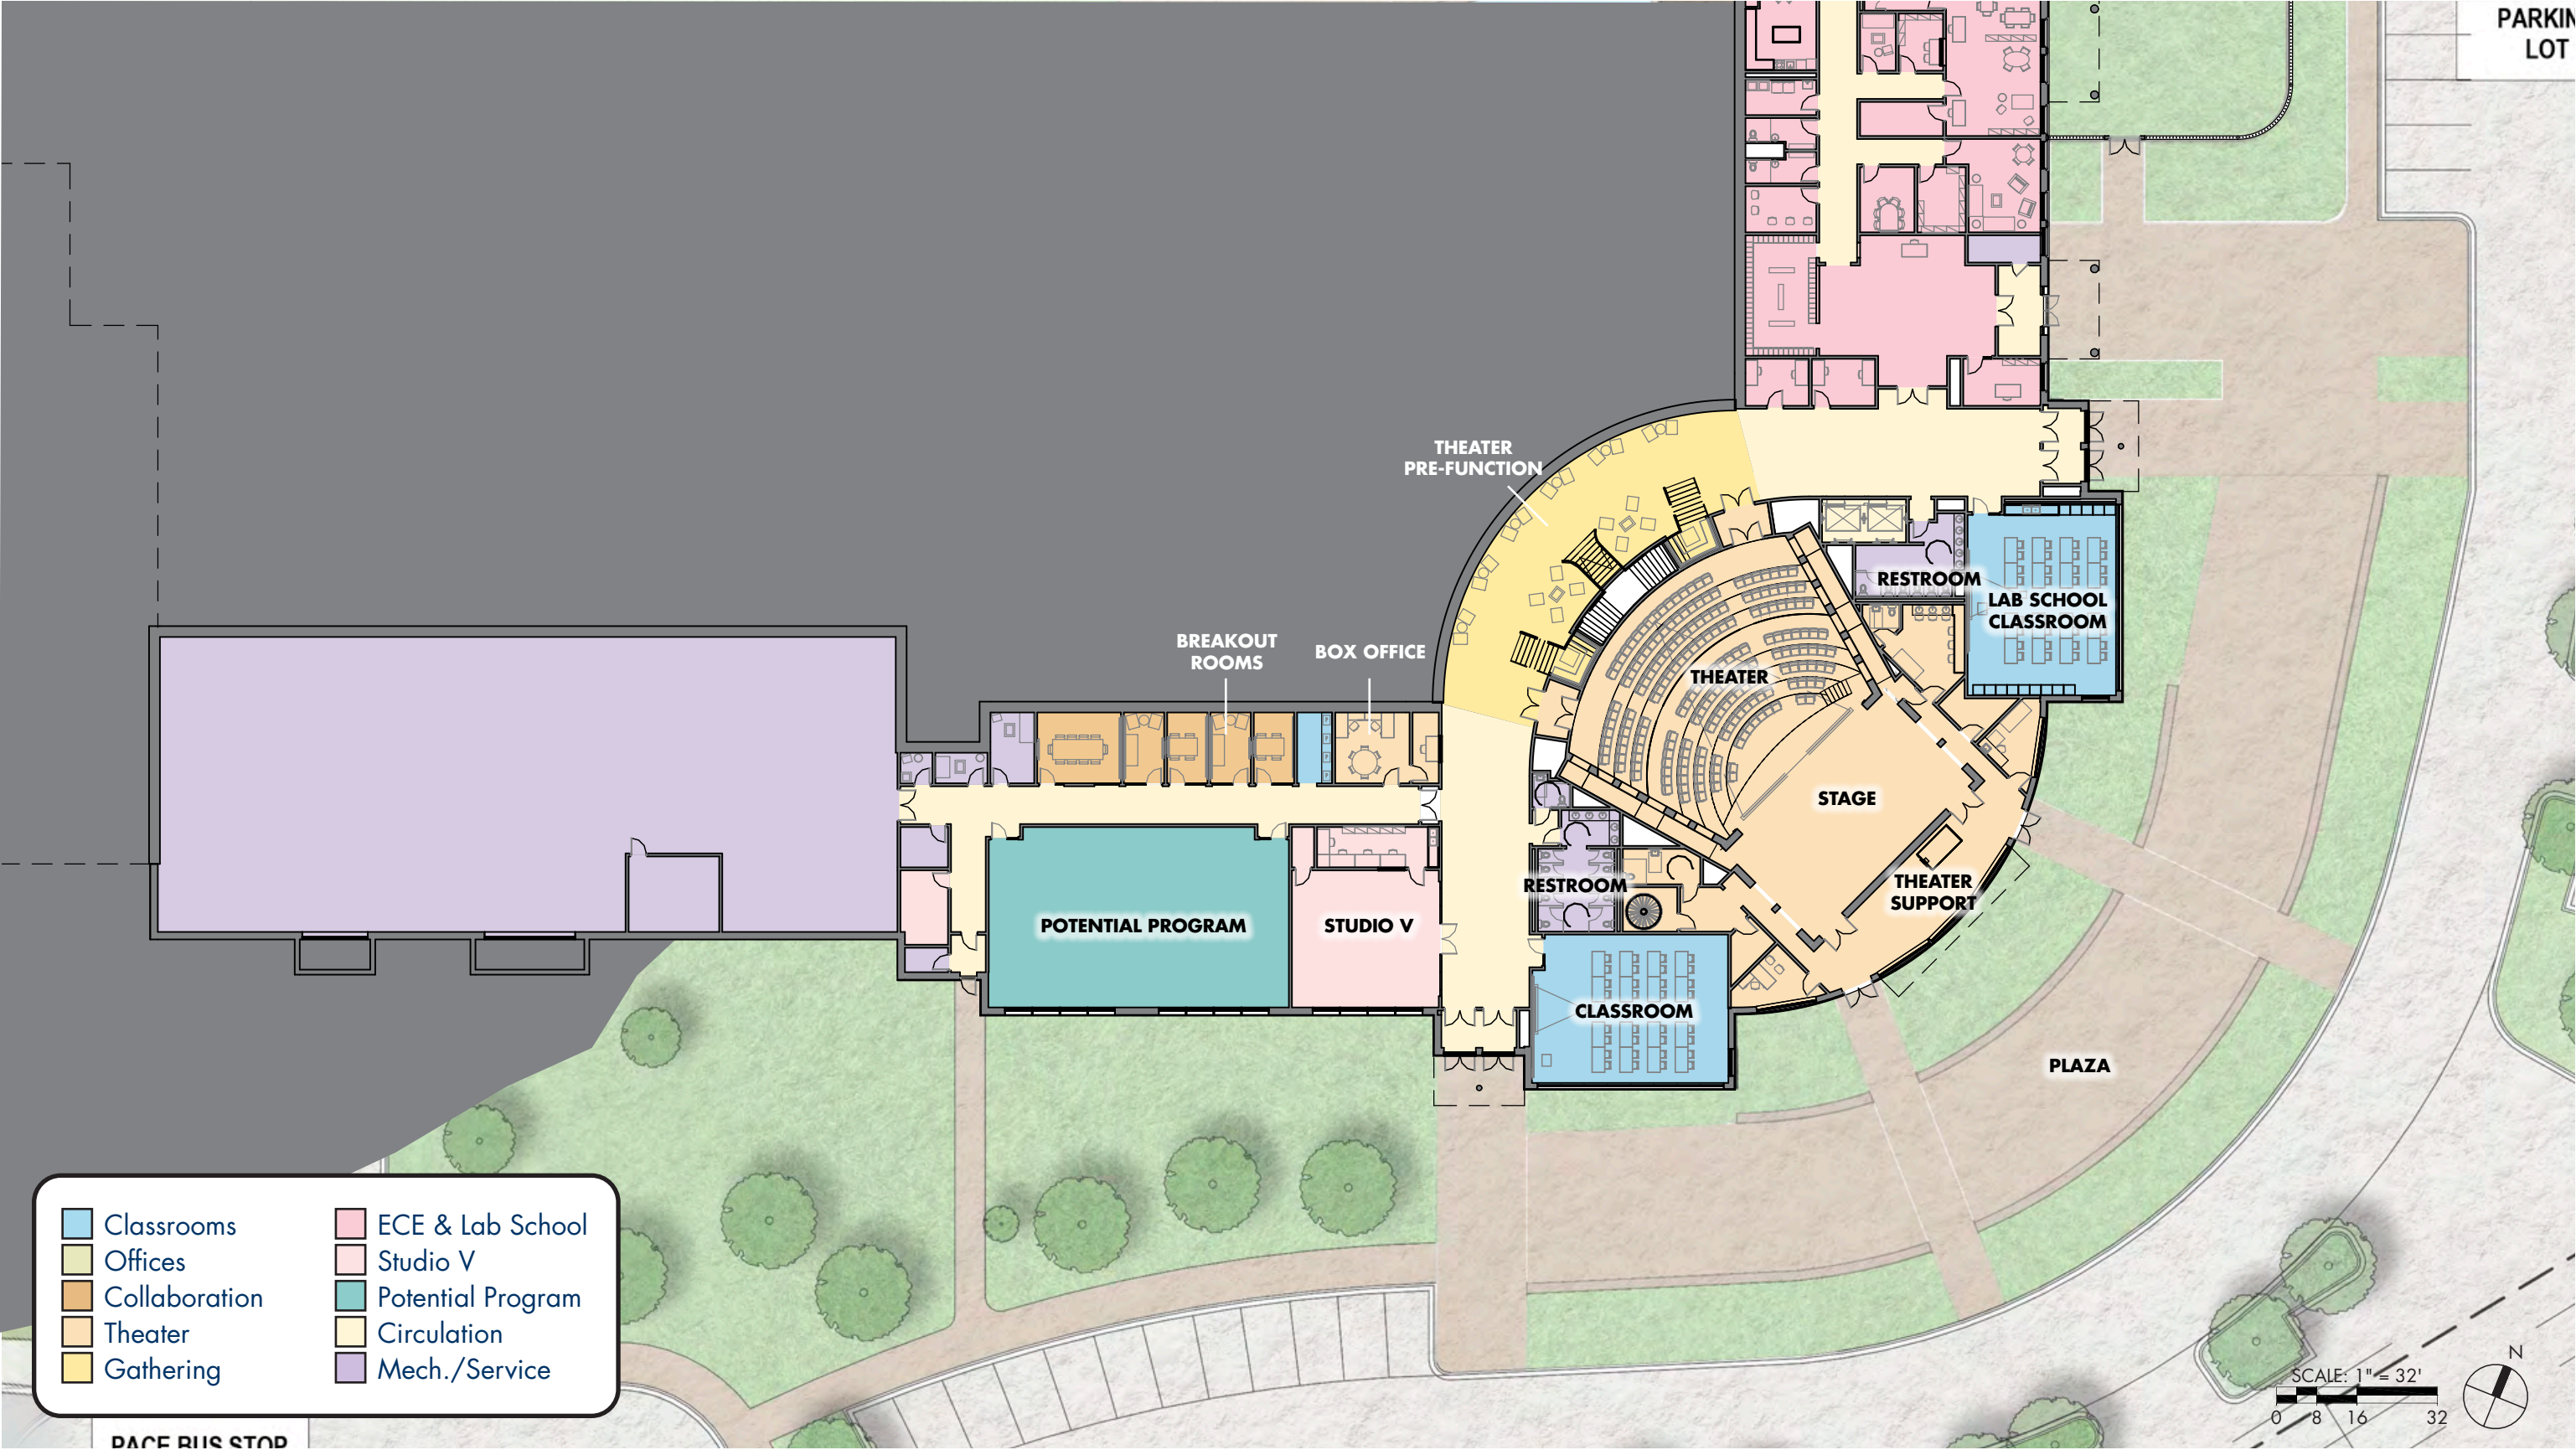

CLASSROOMS & OFFICES

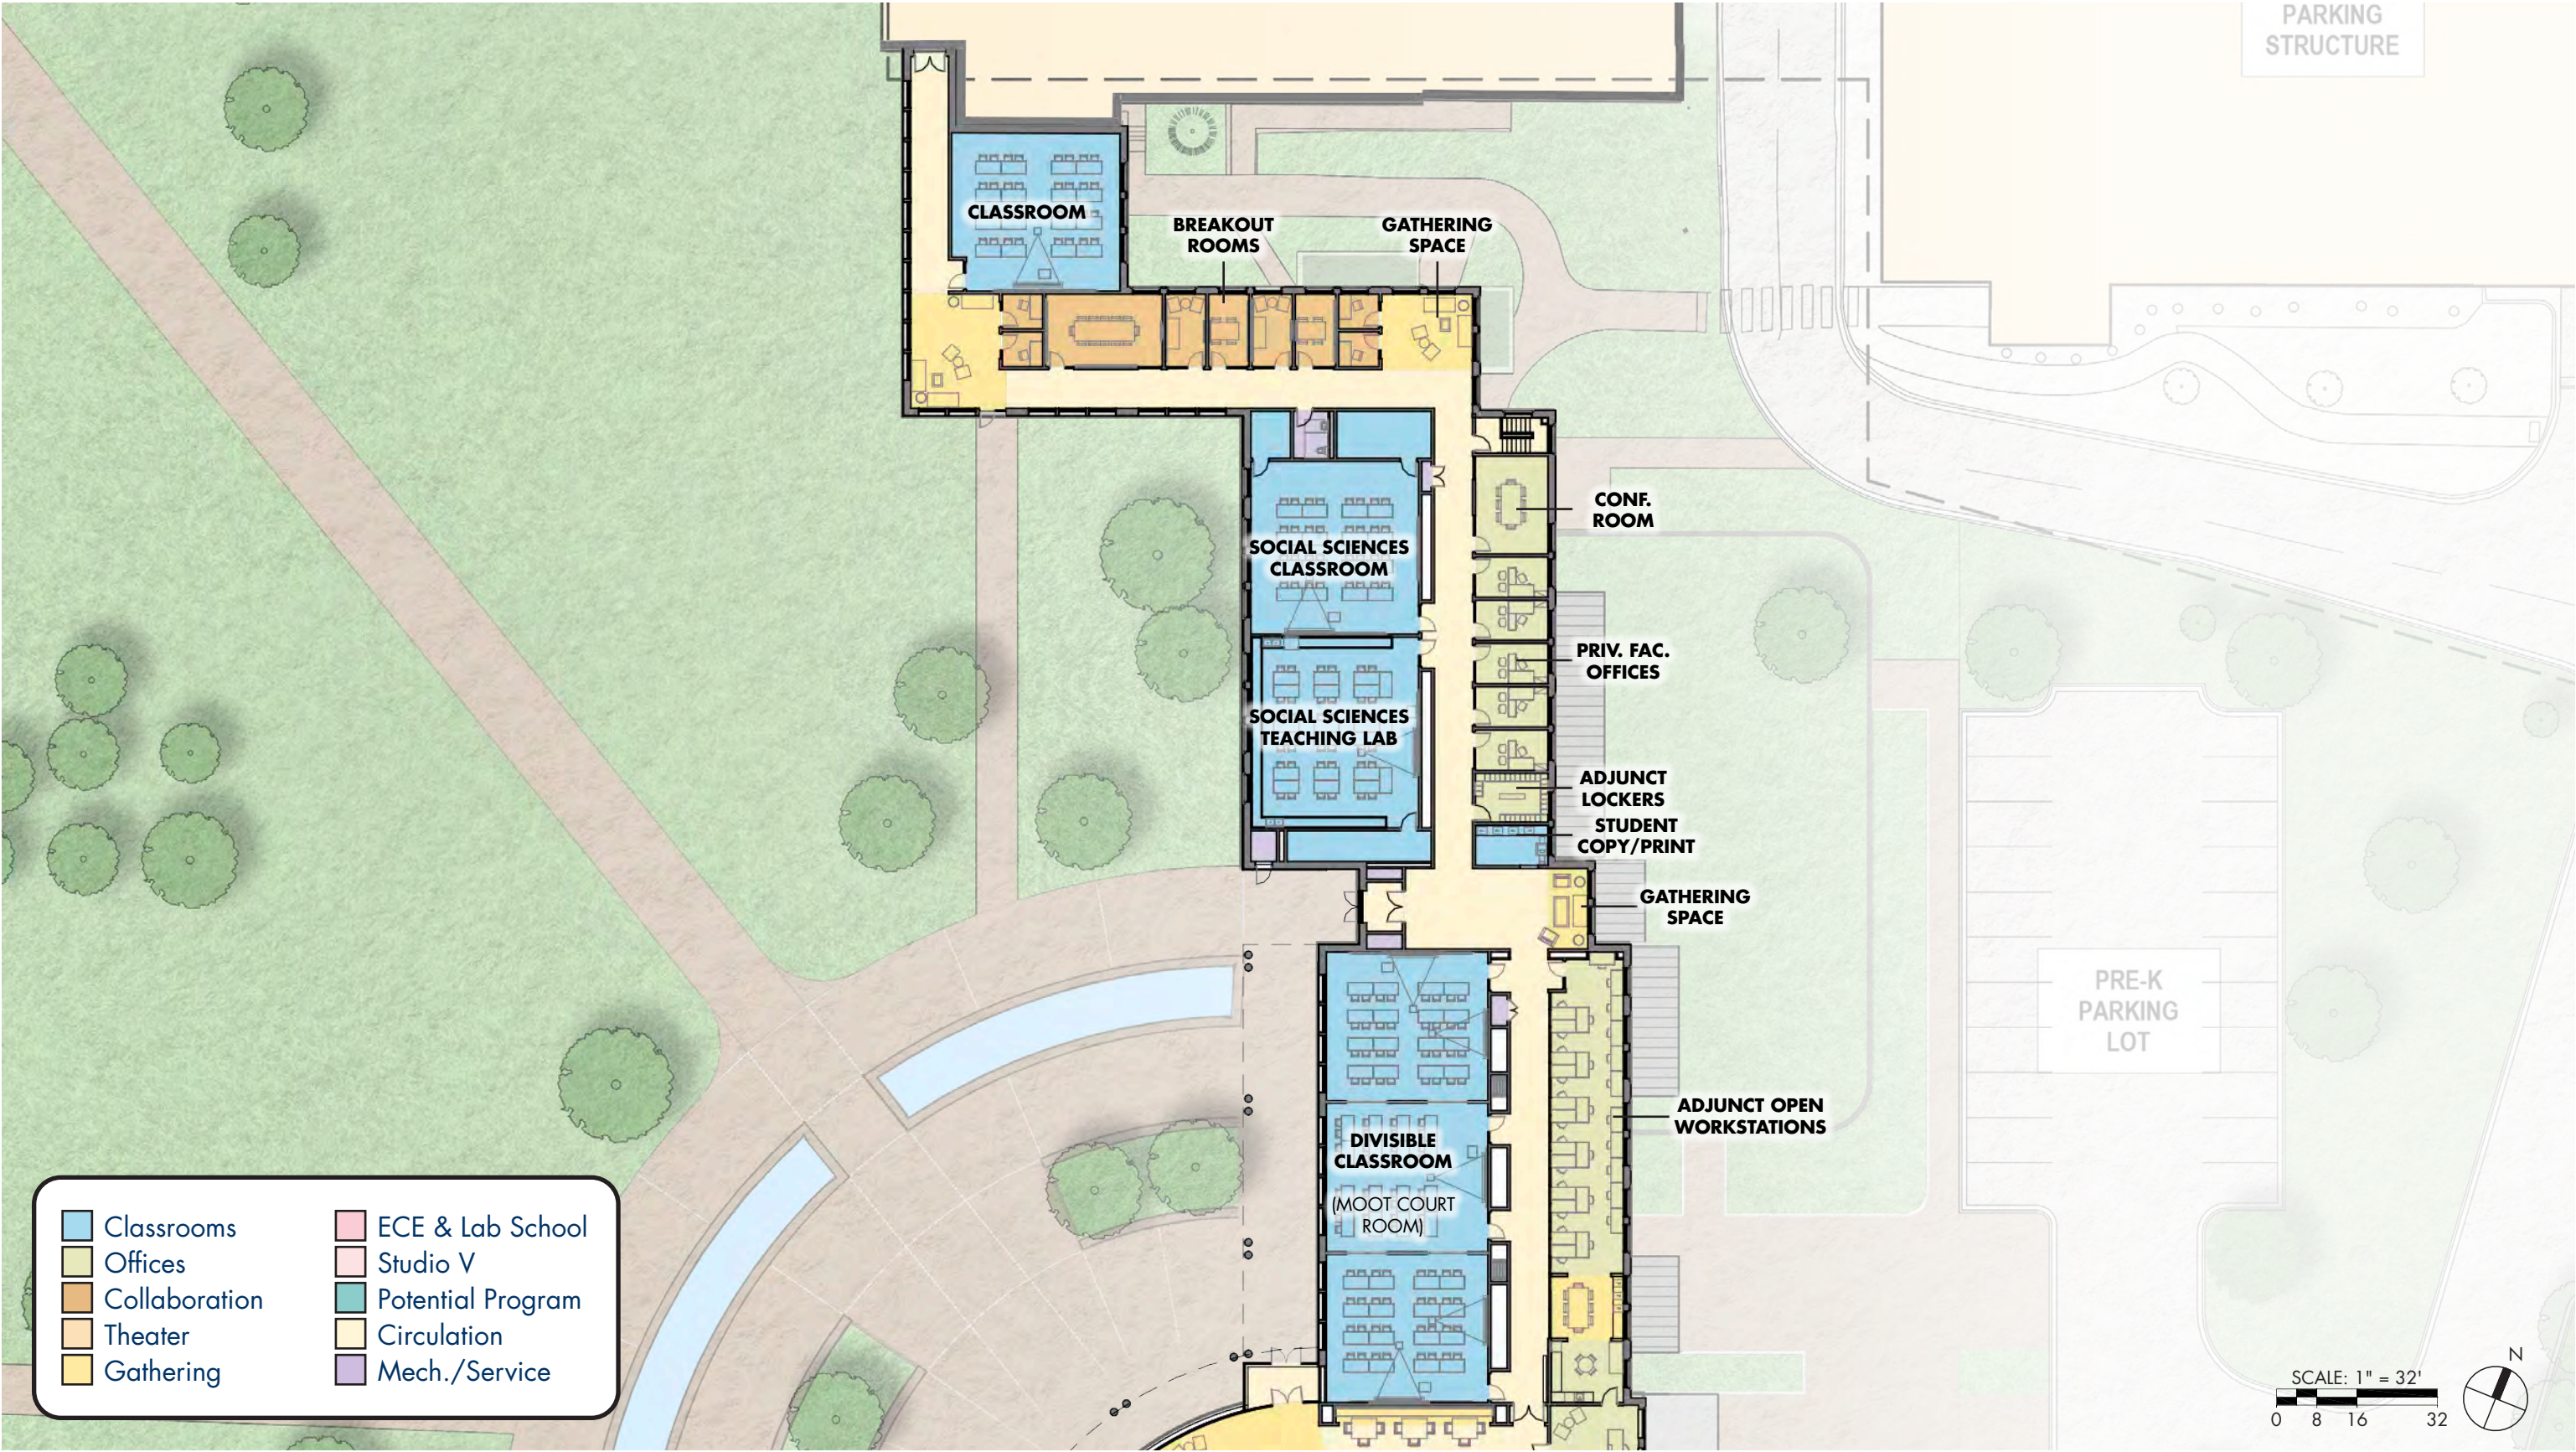


THEATER, CLASSROOMS & OFFICES

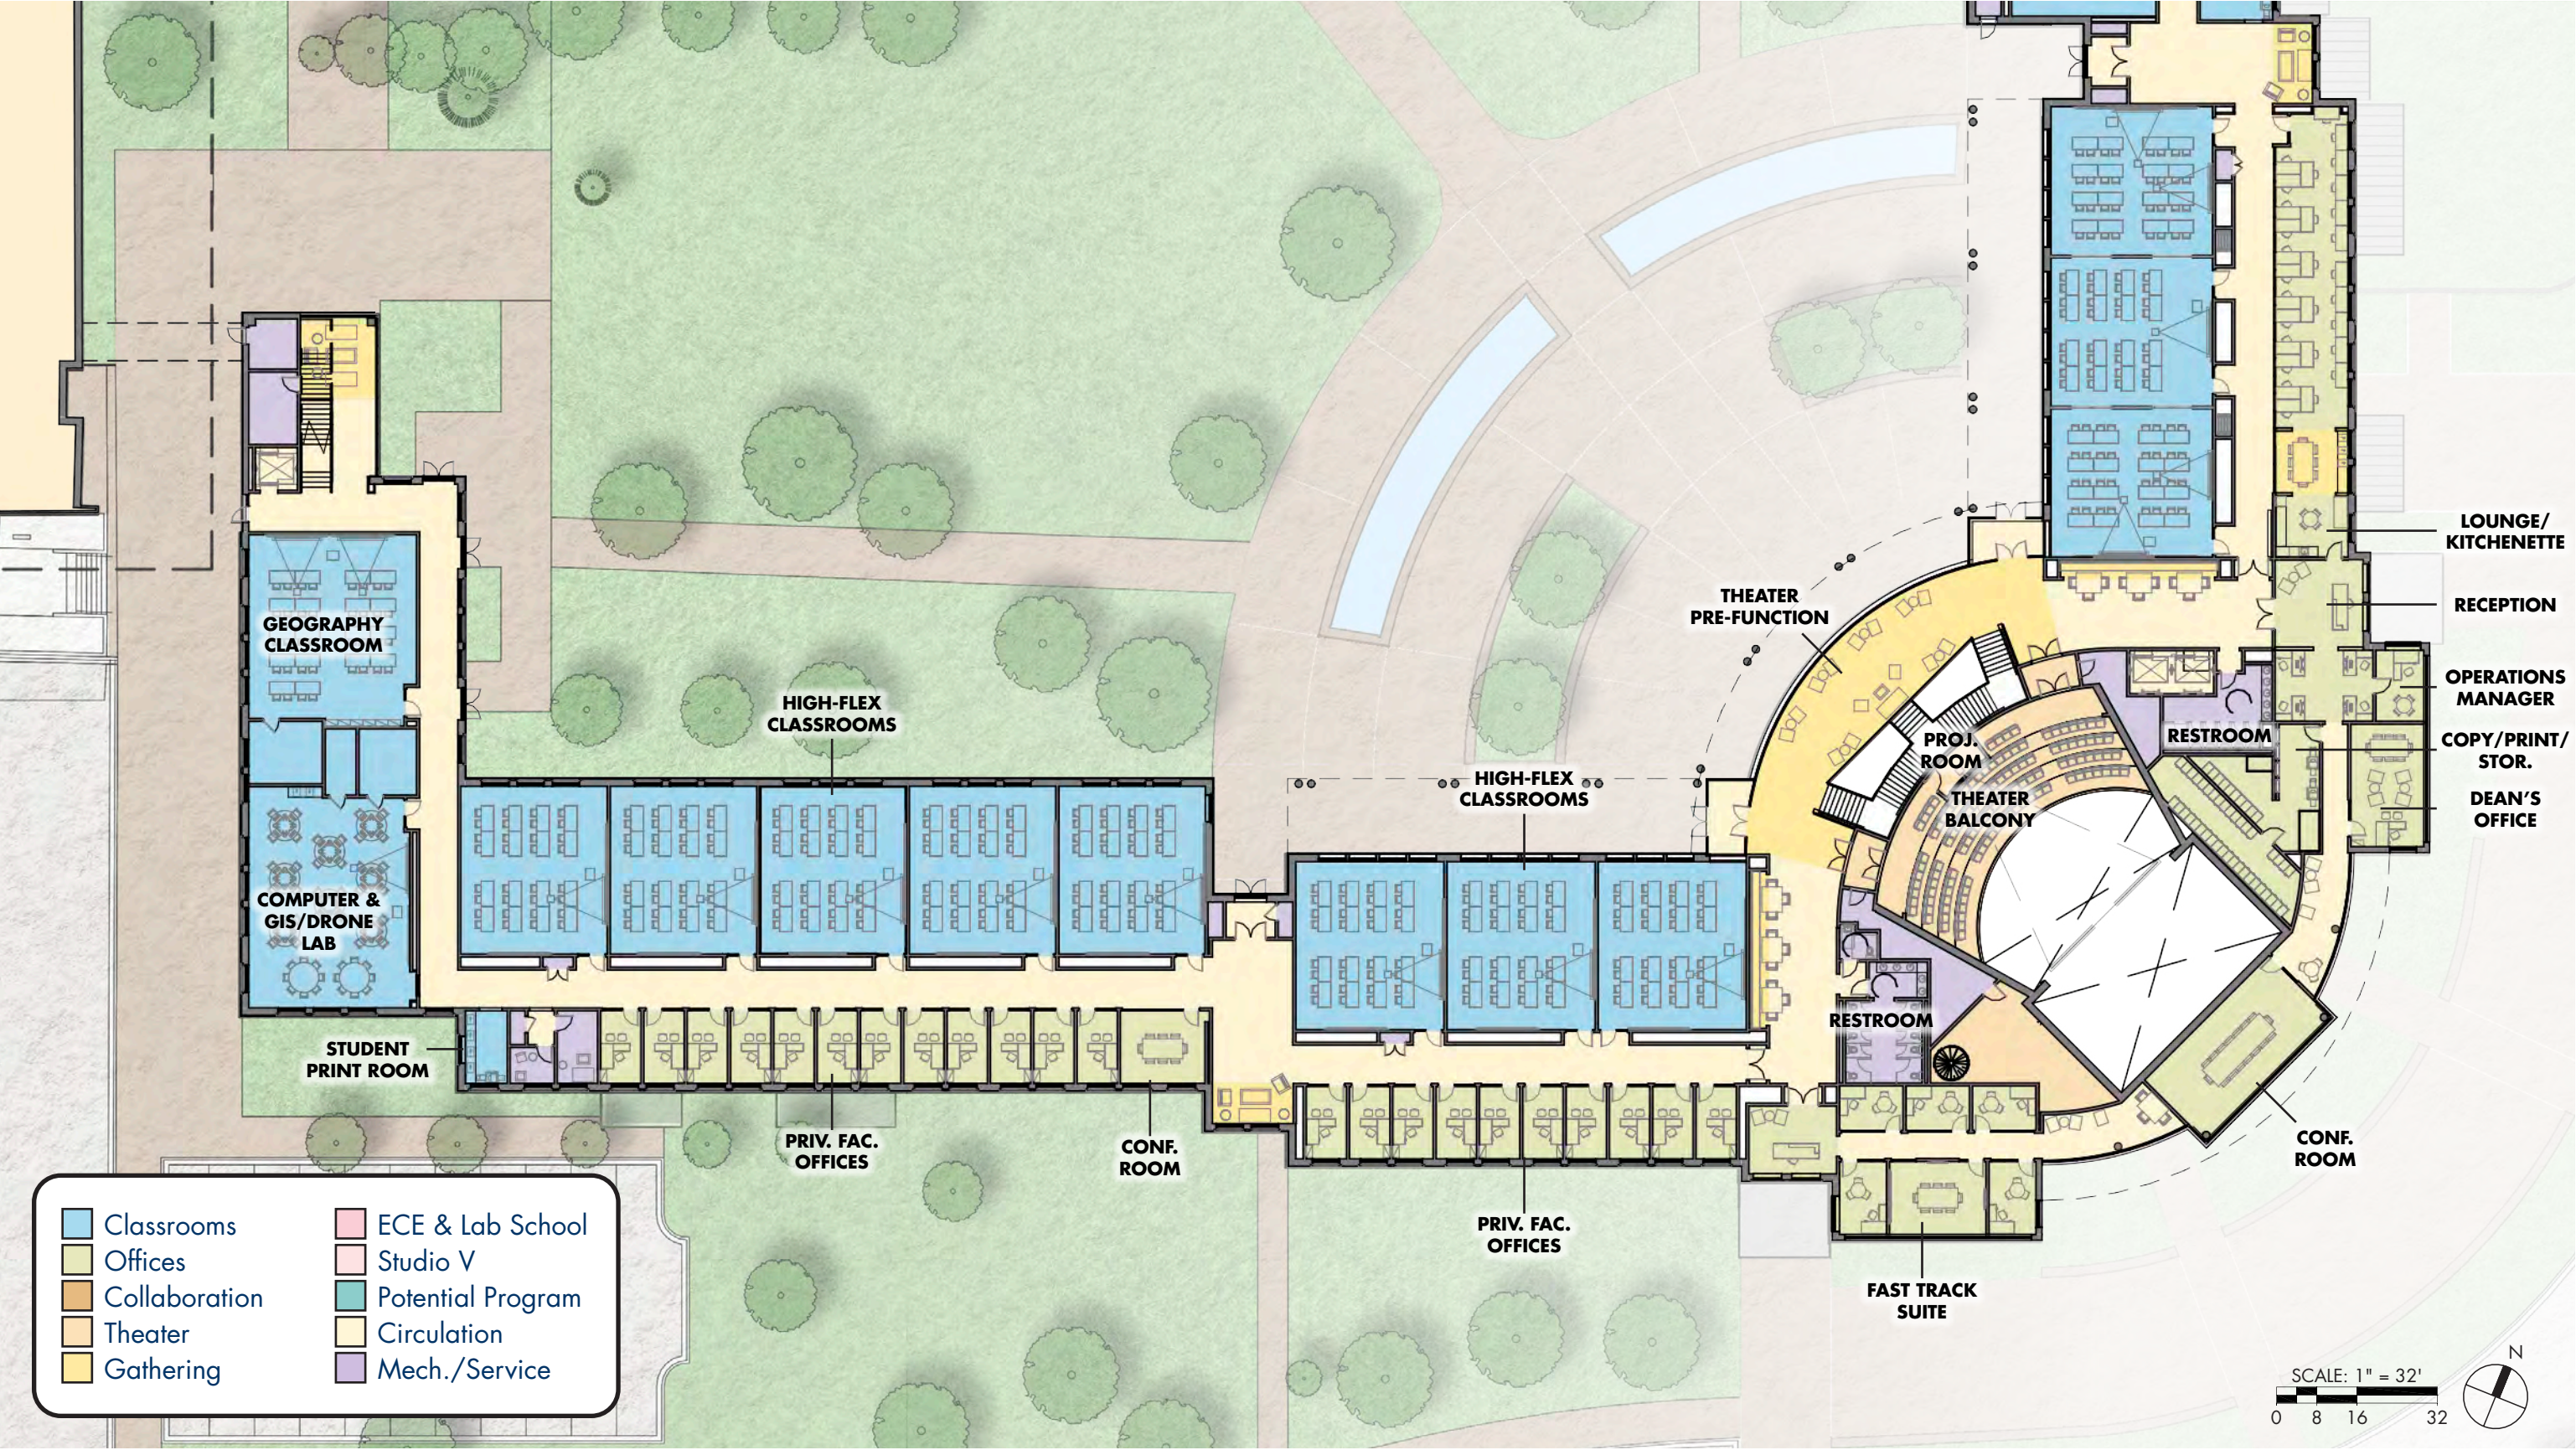






EAST ELEVATION

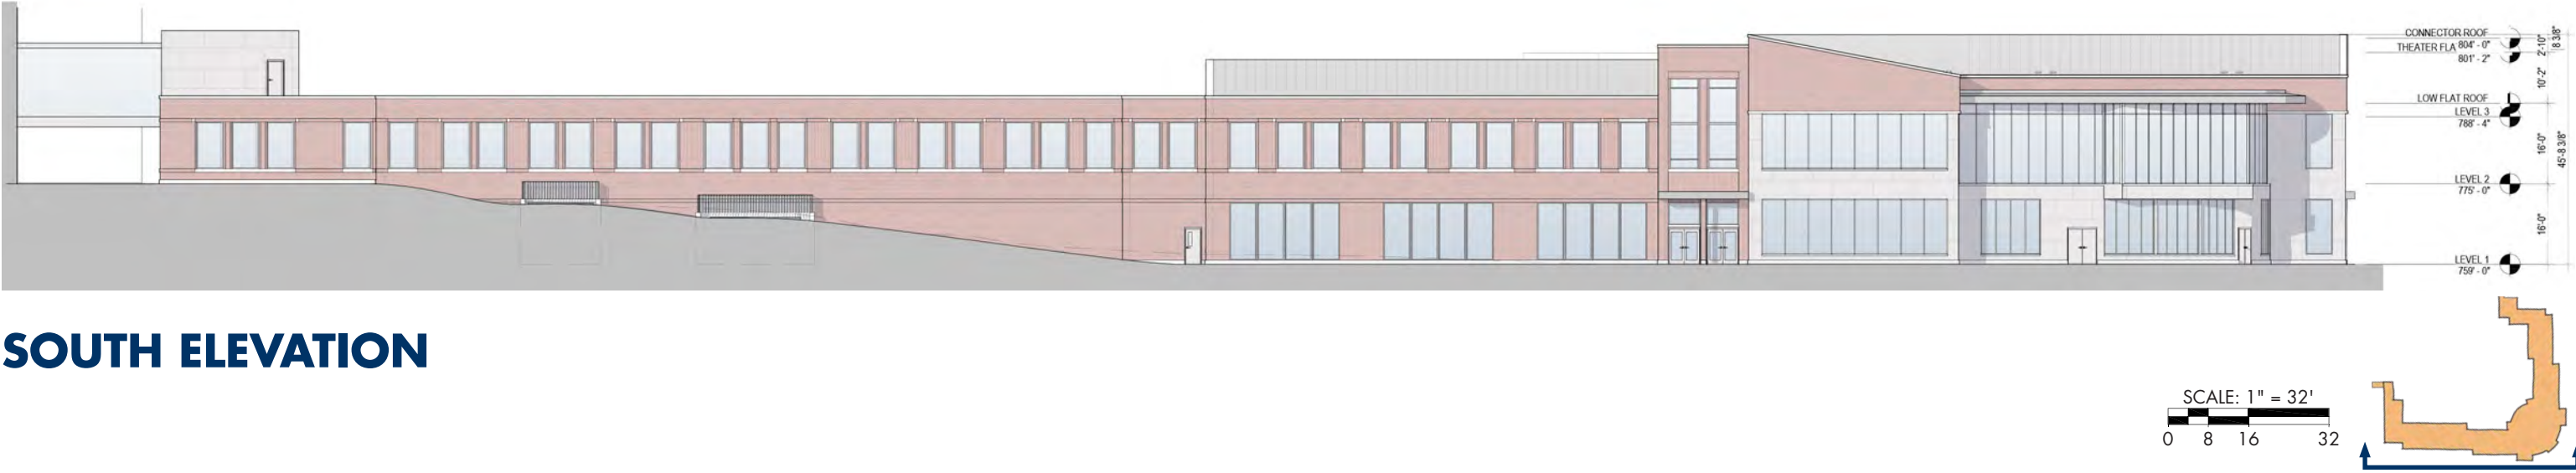



SOUTH ELEVATION

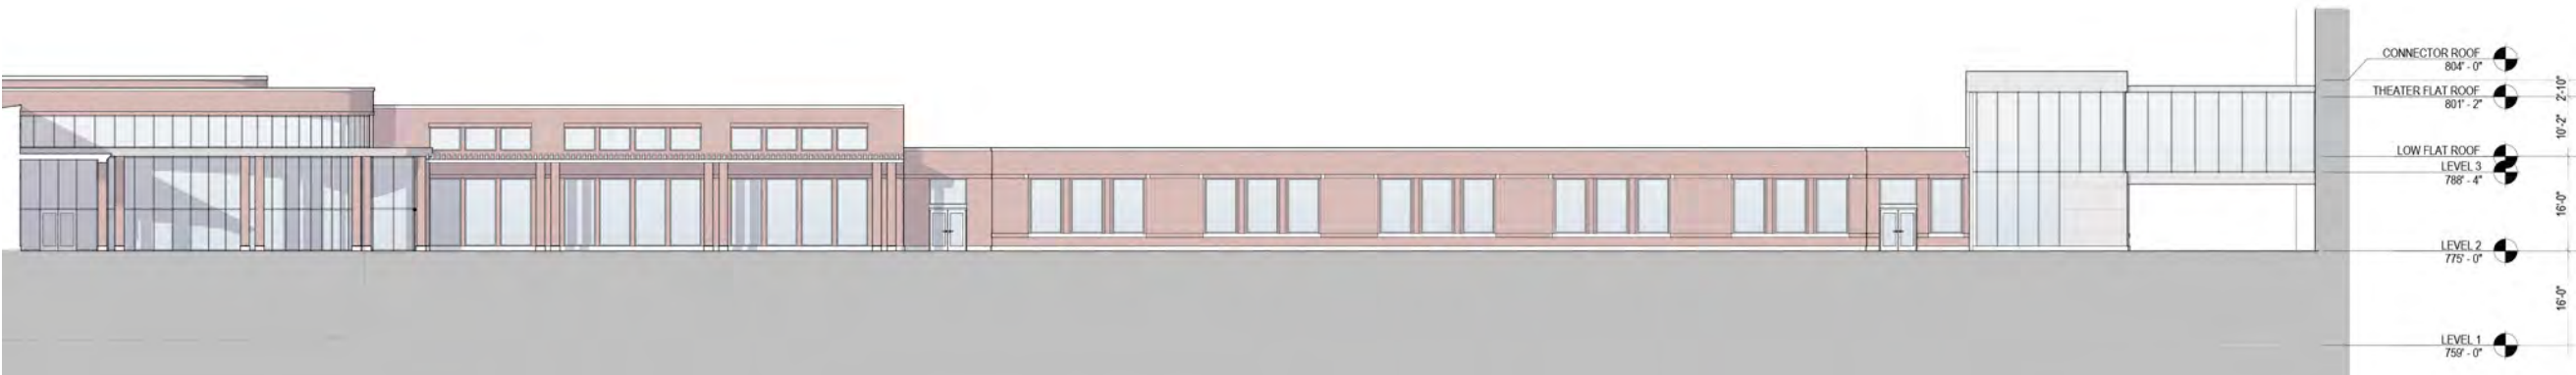

NORTH COURTYARD ELEVATION

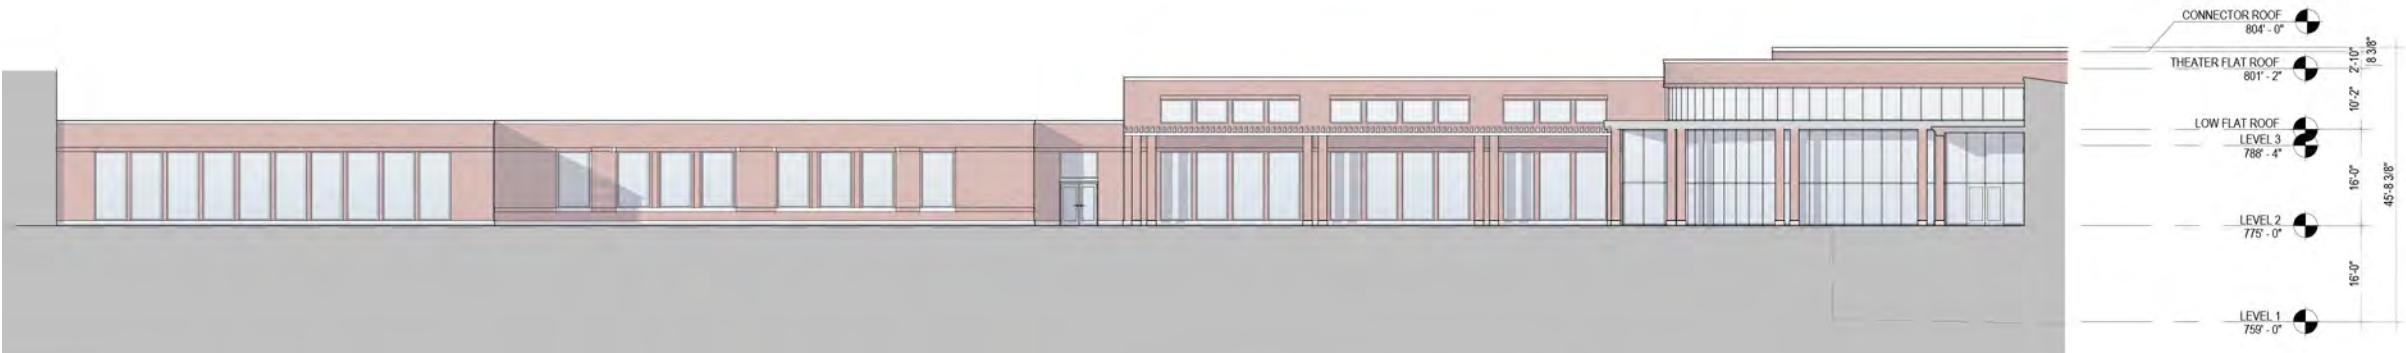

WEST COURTYARD ELEVATION



VIEW FROM SOUTHEAST



VIEW FROM NORTHWEST



PRICING UPDATE

PROJECT BUDGET:

CONSTRUCTION COST: **\$62M**

PROJECT COST: **\$78M**

\$13M OVERRUN IN CONSTRUCTION COST


MAIN DRIVERS:

- Theater Equipment
- Stormwater Retention
- Complexity of Phasing

PRICING UPDATE

NEXT STEPS:

- Reconcile estimates from Design Team and Construction Manager
- Review phasing and temporary conditions
- Review Potential Alternates and Cost Strategies
- Recommendations to the College

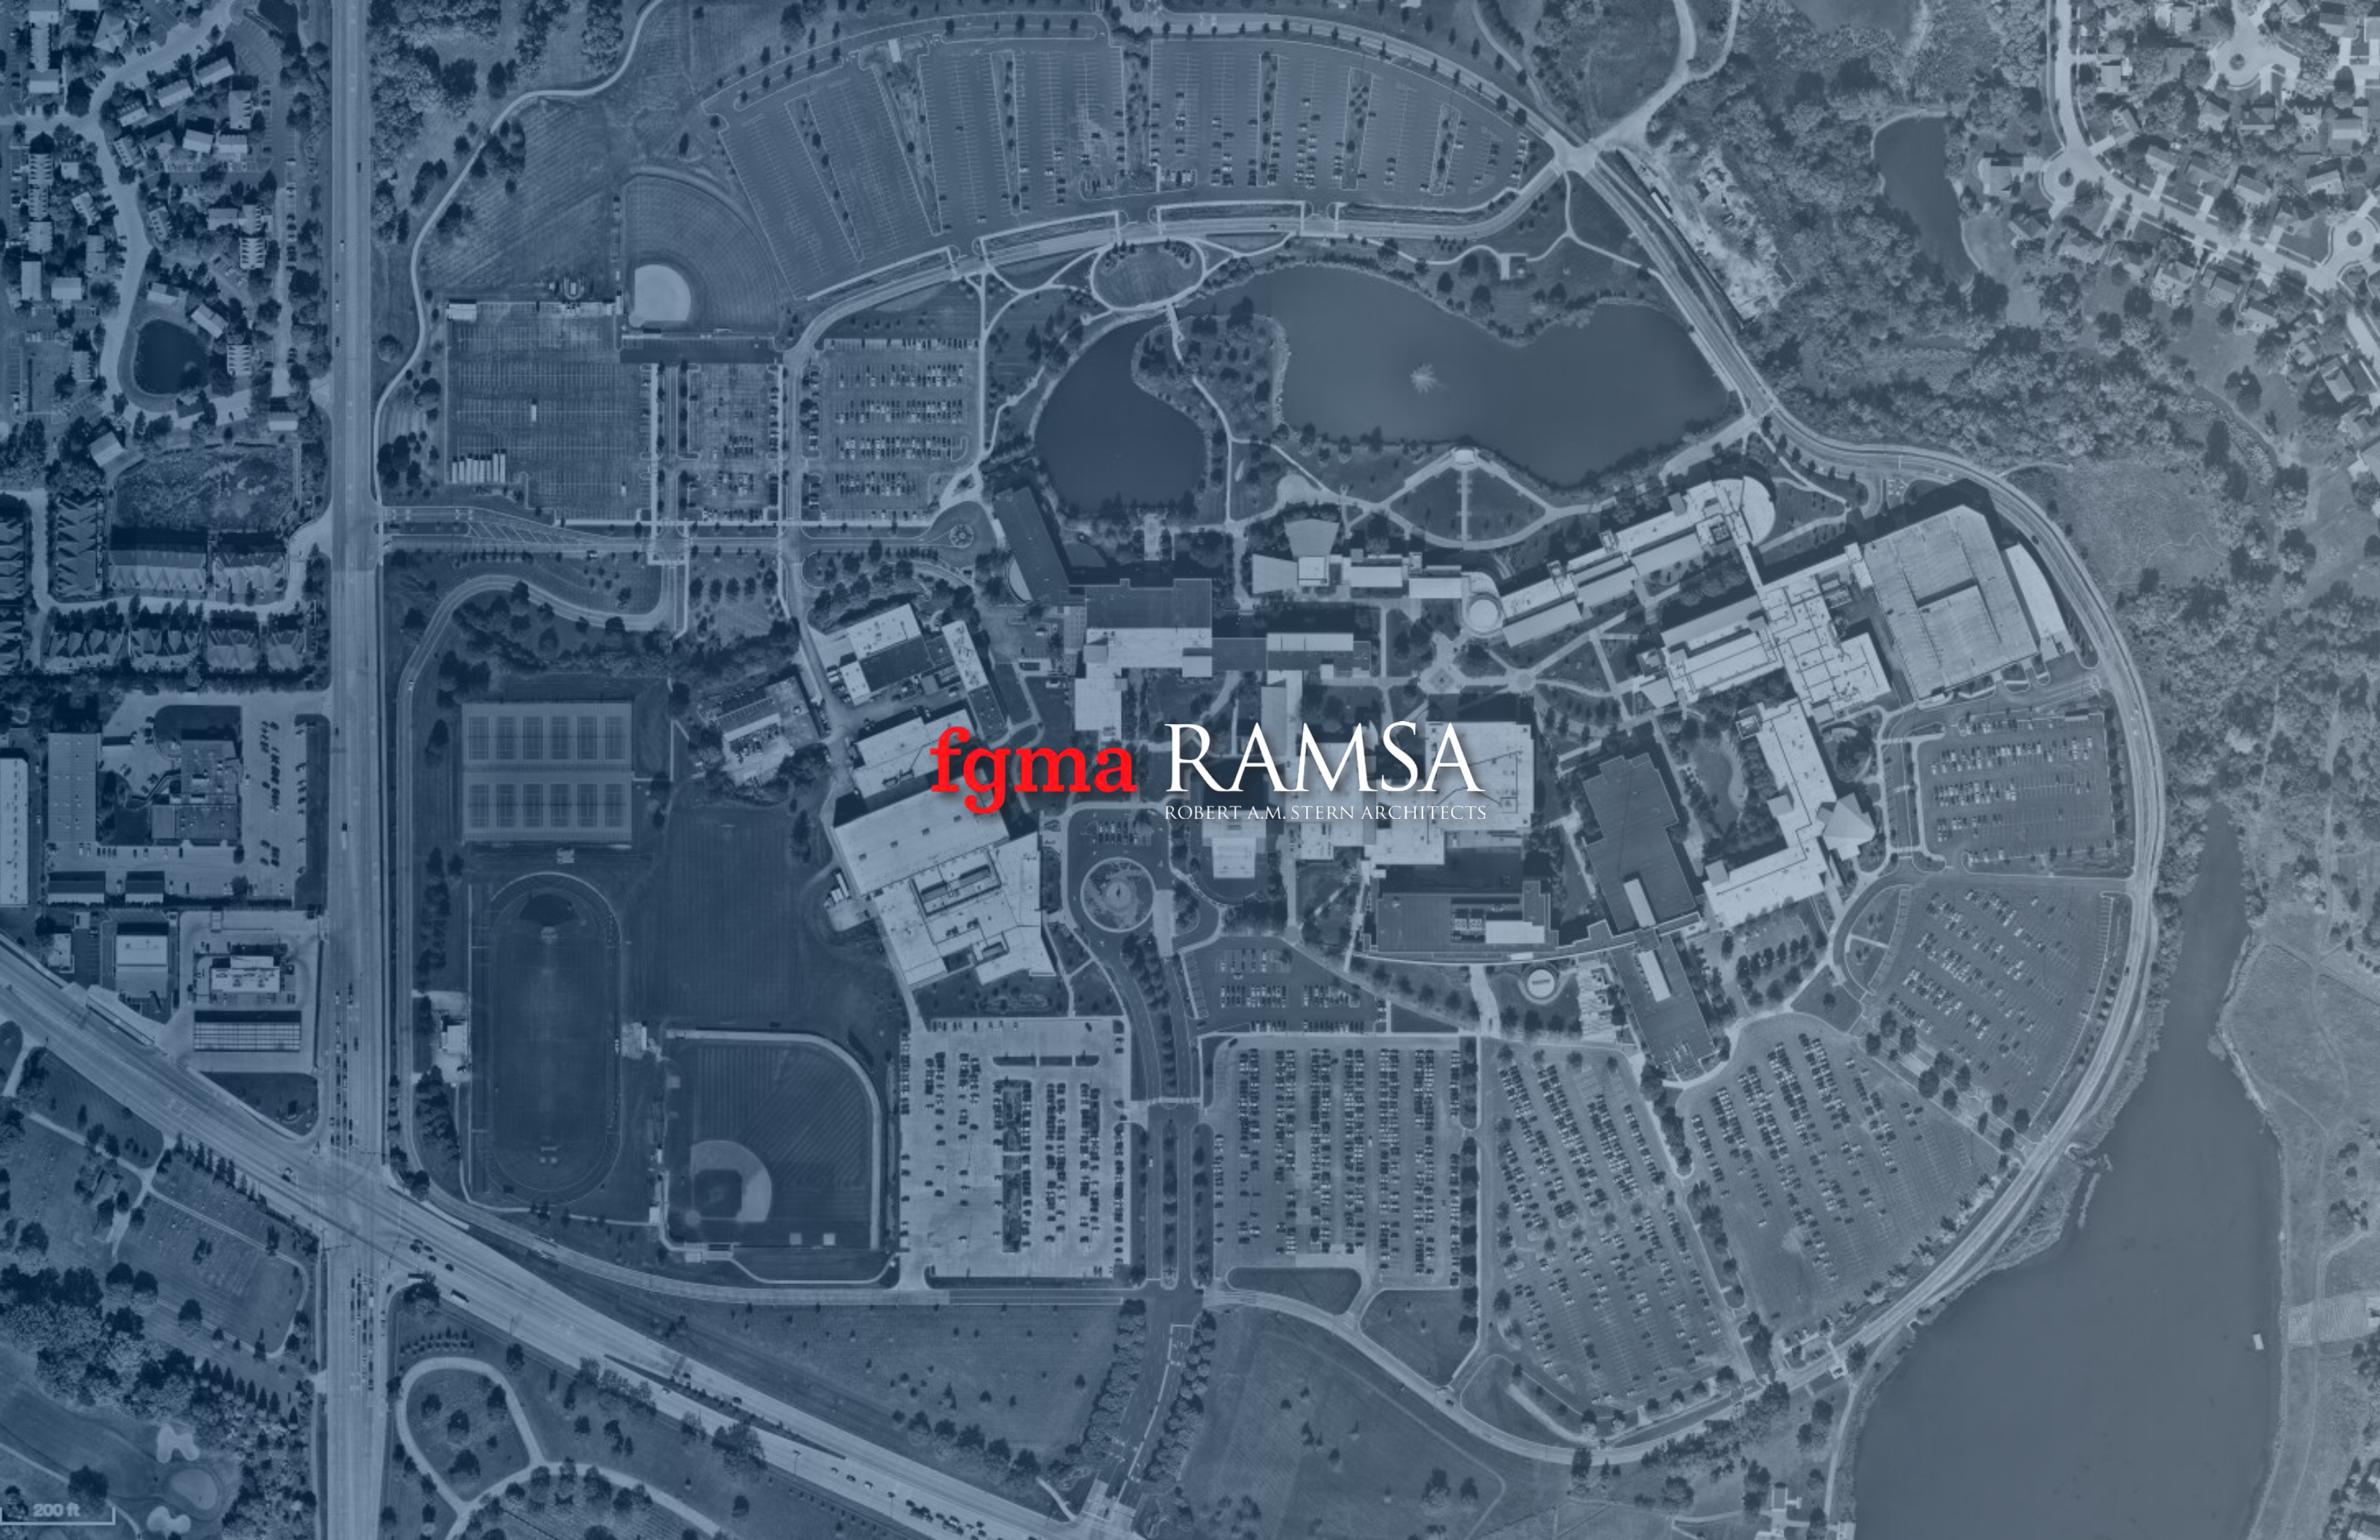

fgma RAMSA
ROBERT A.M. STERN ARCHITECTS
